The following site is being submitted for inclusion into the GIS registry:

- For DNR County and Region list go to:
  g:\pf\pecfa\site\gis\BRRTS County and Region Codes.xls
- To begin, click on field to the right of *BRRTS ID (no dashes):*.
- Use Tab, ↓ or Pg Down to navigate form. Print & include with file when completed.

This is a:	New Submittal
BRRTS ID (no dashes):	**0310000388**
Comm # (no dashes):	54446974821
County:	Clark
Region:	West Central
Site name:	Loyal DC 66 Service
Street Address:	521 N Main St
City:	Loyal
Final Closure Date	2001-12-17
Closure Conditions:	met
Off-source property contamination?	No
(If yes, attach locational data and deed information on pg. 2)	
Right-of-way contamination?	Yes
Contaminated media:	Groundwater

GPS Coordinates (meters in the **WTM91** projection)

Easting (X):	480720.000000000
Northing (Y):	474319.000000000
Collection Method:	
Scale or Resolution:	1:08,000

(1:24,000 scale or finer) ("**1:**" and comma is default)

Prepared by:	
Submitted by:	Cheryl Nelson

Source Property Checklist

- ☒ Final Closure Letter
- ☒ Copy of the most recent deed, which includes legal description for all properties w/ GW > NR 140 ES
- ☐ Where the legal description in the deed(s) refers to a certified survey map or recorded plat map, include those documents
- ☒ Parcel ID for all properties w/ GW > NR 140 ES
- ☒ General Location Map
- ☒ Detailed Location Map showing property boundaries, buildings, MW(s) and/or potable wells etc for properties with GW >NR140 ES
- ☒ Latest Map(s) showing extent or outline of current GW plume (isoconcentrations)
- ☒ Map showing GW flow direction
- ☒ Latest Table of GW results
- ☒ Geologic cross section (if generated as part of the site investigation)
- ☐ Statement signed by RP certifying correctness of legal descriptions
- ☐ Updated Database

ENVIRONMENTAL & REGULATORY SERVICES
BUREAU OF PECFA
P.O. Box 8044
Madison, Wisconsin 53708-8044
TDD #: (608) 264-8777
Fax #: (608) 267-1381
http://www.commerce.state.wi.us
http://www.wisconsin.gov
Scott McCallum, Governor
Philip Edw. Albert, Acting Secretary

Wisconsin
Department of Commerce

December 17, 2001

Jack Wild
Abbotsford Oil Co Inc
402 E Spruce St
PO Box F
Abbotsford, WI 54405-0906

RE: **Final Closure**

Commerce # 54446-9748-21 WDNR BRRTS # 03-10-000388
Loyal DC 66 Service, 521 N Main St, Loyal

Dear Mr. Wild:

This letter acknowledges receipt of the information requested in the Wisconsin Department of Commerce's (Commerce) PECFA Site Review Section May 7, 2001, *Conditional Closure* letter. On November 28, 2001, Commerce received the monitoring well abandonment forms for MW-1 through MW-3; MW 5 through 9; PW1 and PW-2; and wells VP-1, VW-2, VW-3 and VW-3A. On October 31, 2001, Commerce received a filed copy of the soil deed affidavit and groundwater use restriction as well as both notification of Right-Of-Way contamination for the City of Loyal and the Department of Transportation. Please note that Commerce is making no determination as to the accuracy of the legal description information. It is the owner's responsibility to ensure that the property location information is represented correctly. This case is now considered "closed," as described in Commerce's *Conditional Closure* letter.

Please be advised, in reference to PECFA reimbursement (if applicable), that no further action was indicated in the conditional closure letter dated May 7, 2001. As per the recently enacted 2001 Budget Bill language, if the site achieved a "no further remedial action" status before August 31, 2001 and the final PECFA claim is submitted more than 120 days after August 31, 2001, interest costs incurred after January 2, 2002 are ineligible.

In addition, it is in your best interest to keep all documentation related to the investigation and remediation of your site. This information may be needed for future property transactions.

If future site conditions indicate that any remaining contamination poses a threat, and subsequent information indicates a need to reopen this case, any original claim under the PECFA fund would also reopen and you may apply for assistance to the extent of remaining eligibility. If contamination is encountered, appropriate measures must be implemented to assure any residual contamination is managed following all applicable State of Wisconsin regulations and standards.

Thank you for your efforts in protecting Wisconsin's environment. If you have any questions, please contact me in writing at the letterhead address or by telephone at (608) 266-0593.

Sincerely,

Brian F. Taylor
Hydrogeologist
Site Review Section

cc: Ms. Cindy Zelenka, Central Wisconsin Engineers
Case File

497156

Document Number

NOTICE OF CONTAMINATION TO PROPERTY

VOL. 647 PAGE 036

RECORDED ON 07/09/01
AT 3:10p.M. IN VOL. 647
OF RECORDS PAGE 36
CLARK COUNTY WI BY
Lisa Hagedorn

Legal Description of the Property:

See attached legal description recorded in Vol. 290 page 436.

STATE OF WISCONSIN)
) ss
COUNTY OF CLARK)

Recording Area pd $16 Cash

Name and Return Address
Jack Wild
Abbotsford Oil Company, Inc.
P.O. Box F
Abbotsford , WI 54405-0906

Section 1. Abbotsford Oil Company, Inc. is the owner of the above-described property.

Section 2. One or more petroleum discharges have occurred at this property contaminating groundwater above NR 140 enforcement standards, and soils above NR 720 residual contaminant levels (of the Wisconsin Administrative Code) exist(s) on this property. See the attached map labeled Figure 1.

246.0304.000
Parcel Identification Number (PIN)

Section 3. It is the desire and intention of the property owner to impose restrictions on the property which will make it unnecessary to conduct additional soil remediation activities on the property at the present time. The owner hereby declares that all of the property described above is held and shall be held, conveyed or encumbered, leased, rented, used, occupied and improved subject to the following limitations and/or restrictions:

Petroleum-contaminated soil remains on this property. According to the report filed by Central Wisconsin Engineers & Architects, Inc., (CWEA) dated April 2, 2001, the residual contaminated soils are located in the eastern half of the site. Natural attenuation is the approved remedial alternative for this site. An impermeable cap or cover is the selected remedial action to address residual soil contamination on the property. Therefore, an impermeable cap or cover (i.e. concrete, asphalt) shall be maintained across this property until: 1). The soil is actively remediated or removed or; 2). It can be shown that the soil has naturally degraded to levels shown to be protective of the environment and human health. If subsurface work is done in the contaminated areas, the contamination shall be properly treated or disposed of in accordance with applicable laws. File references: PECFA Claim number 54446-9748-21 and BRRTS 03-10-000388, CWEA report dated April 2, 2001.

Section 4. Anyone who proposes to construct or reconstruct a well on this property is required to contact the Department of Natural Resources' Bureau of Drinking Water and Groundwater, or its successor agency, to determine what specific prohibitions or requirements are applicable, prior to constructing or reconstructing a well on this property. No well may be constructed or reconstructed on this property unless applicable requirements are met.

Any person who is or becomes owner of the property described above may request that the Wisconsin Department of Commerce, or its successor, issue a determination that the restrictions set forth in this covenant are no longer required. That property owner shall provide any and all necessary information to the Department in order for the Department to be able to make a determination. Upon receipt of such a request, the Department shall determine whether or not the restrictions contained herein can be extinguished. Conditions under which a restriction may be extinguished will be determined in accordance with the site specific standards, rules and laws for this property. If the Department determines that the restrictions can be extinguished, an affidavit, with a copy of the Department's written determination, may be recorded to give notice that this restriction, or portions of this restriction are no longer binding. Any restriction placed upon this property shall not be extinguished without the Department's written determination.

IN WITNESS WHEREOF, the owner of the property has executed this document, this 9th day of July, 2001.

By signing this document, Jack Wild, acknowledges that he is duly authorized to sign this document on behalf of Abbotsford Oil Company, Inc.

Signature: Jack Wild

Print Name: Jack Wild

Title: Owner

Subscribed and sworn to before me this 9TH day of JULY, 2001.

Lois M Hagedorn, LOIS M. HAGEDORN

Notary Public, State of Wisconsin

My commission HAGE EXPIRES 12-07-03

LOIS M. HAGE NOTARY PUBLIC STATE OF

This document was drafted by the Wisconsin Department of Commerce.

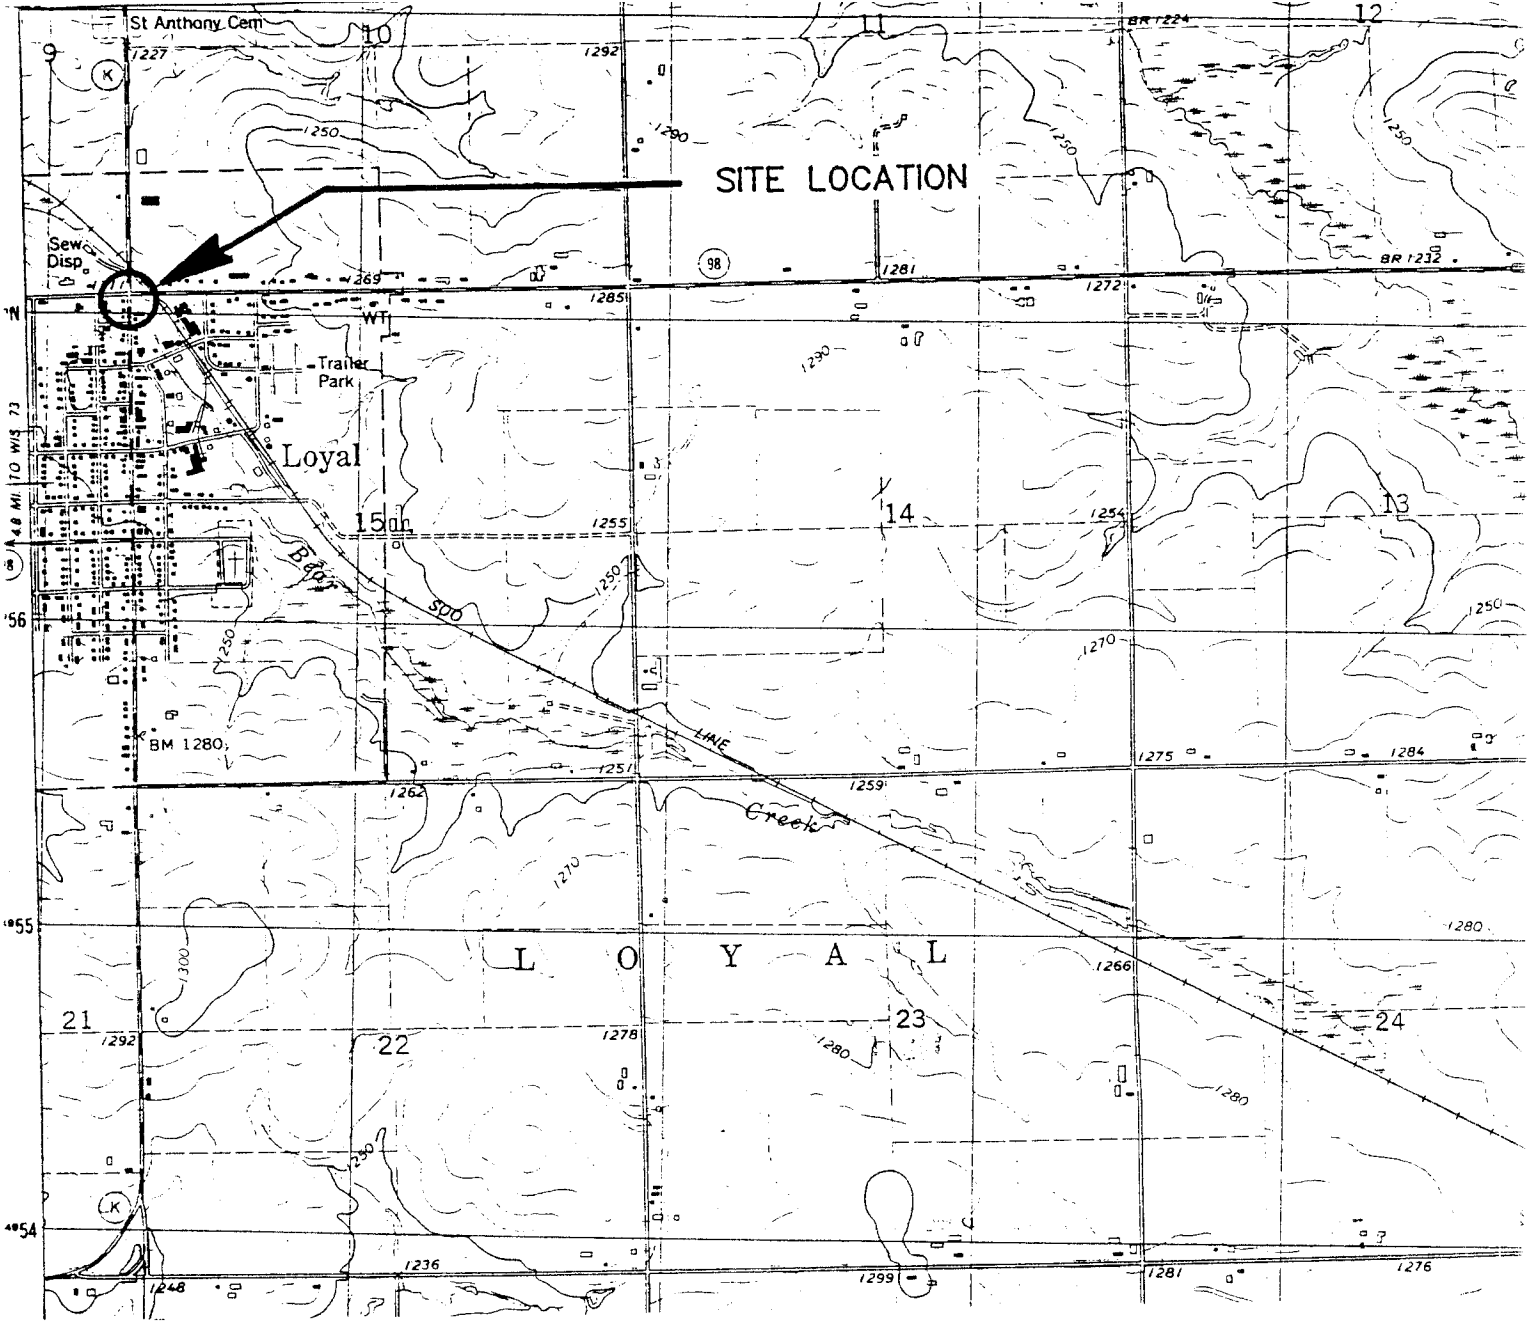

SOURCE:
U.S.G.S. QUADRANGLE MAP
"LOYAL EAST, WIS."
1979

N

SCALE: 1:24000

0 1/2 1 MILE

NO	BY	DATE	REVISION	APP'D

SHEET TITLE: SITE LOCATION MAP

PROJECT:
LOYAL DC 66
LOYAL, WISCONSIN

CENTRAL WISCONSIN ENGINEERS, INC.

DRAWN BY: R.H.
CHECKED BY: SSG
APPROVED BY: M.J.
DATE: 2/95

FIGURE 1

PROJ. NO. 13090070
DNR NO. WD/UD 388

AME AND ARCHITECTS, INC.
CENTRAL WISCONSIN ENGINEERS
PHONE: (715) 359-9400
5707 SCHOFIELD AVENUE
FAX: (715) 355-4199
WESTON, WISCONSIN 54476

PROJECT:
ESTIMATED EXTENT OF RESIDUAL SOIL AND GROUNDWATER CONTAMINATION
LOYAL 66 SERVICE STATION
LOYAL, WISCONSIN

DRAWN BY: H.S.
CHECKED BY:
APPROVED BY:
DATE: 05/01
PROJECT NO: 13090070
DNR NO: 03-10-000388

FIGURE: 1

CAD FILE:

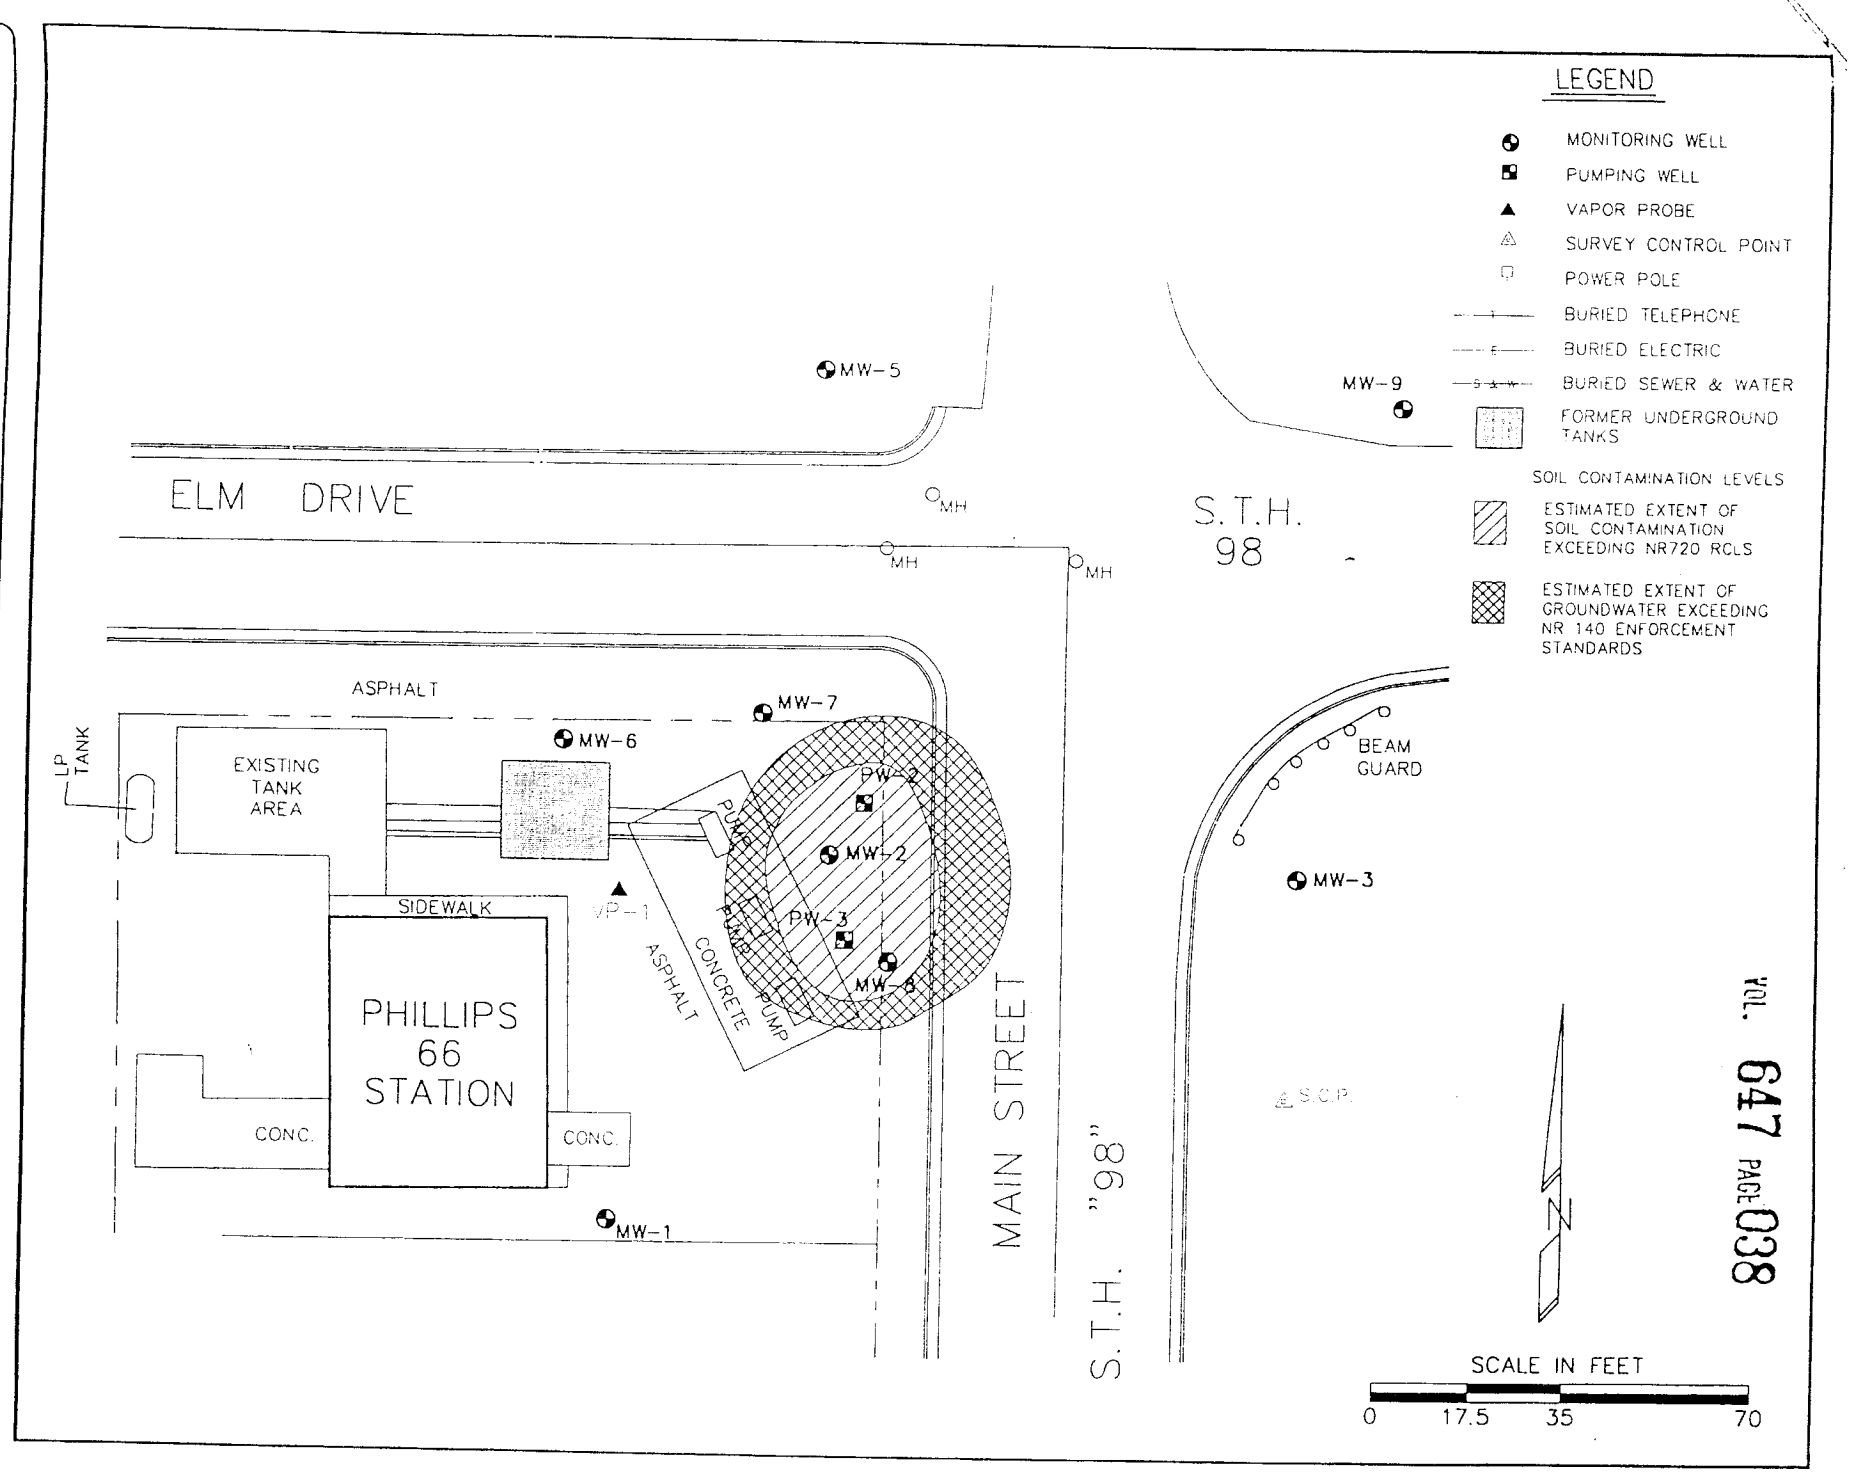

VOL. 647 PAGE 038

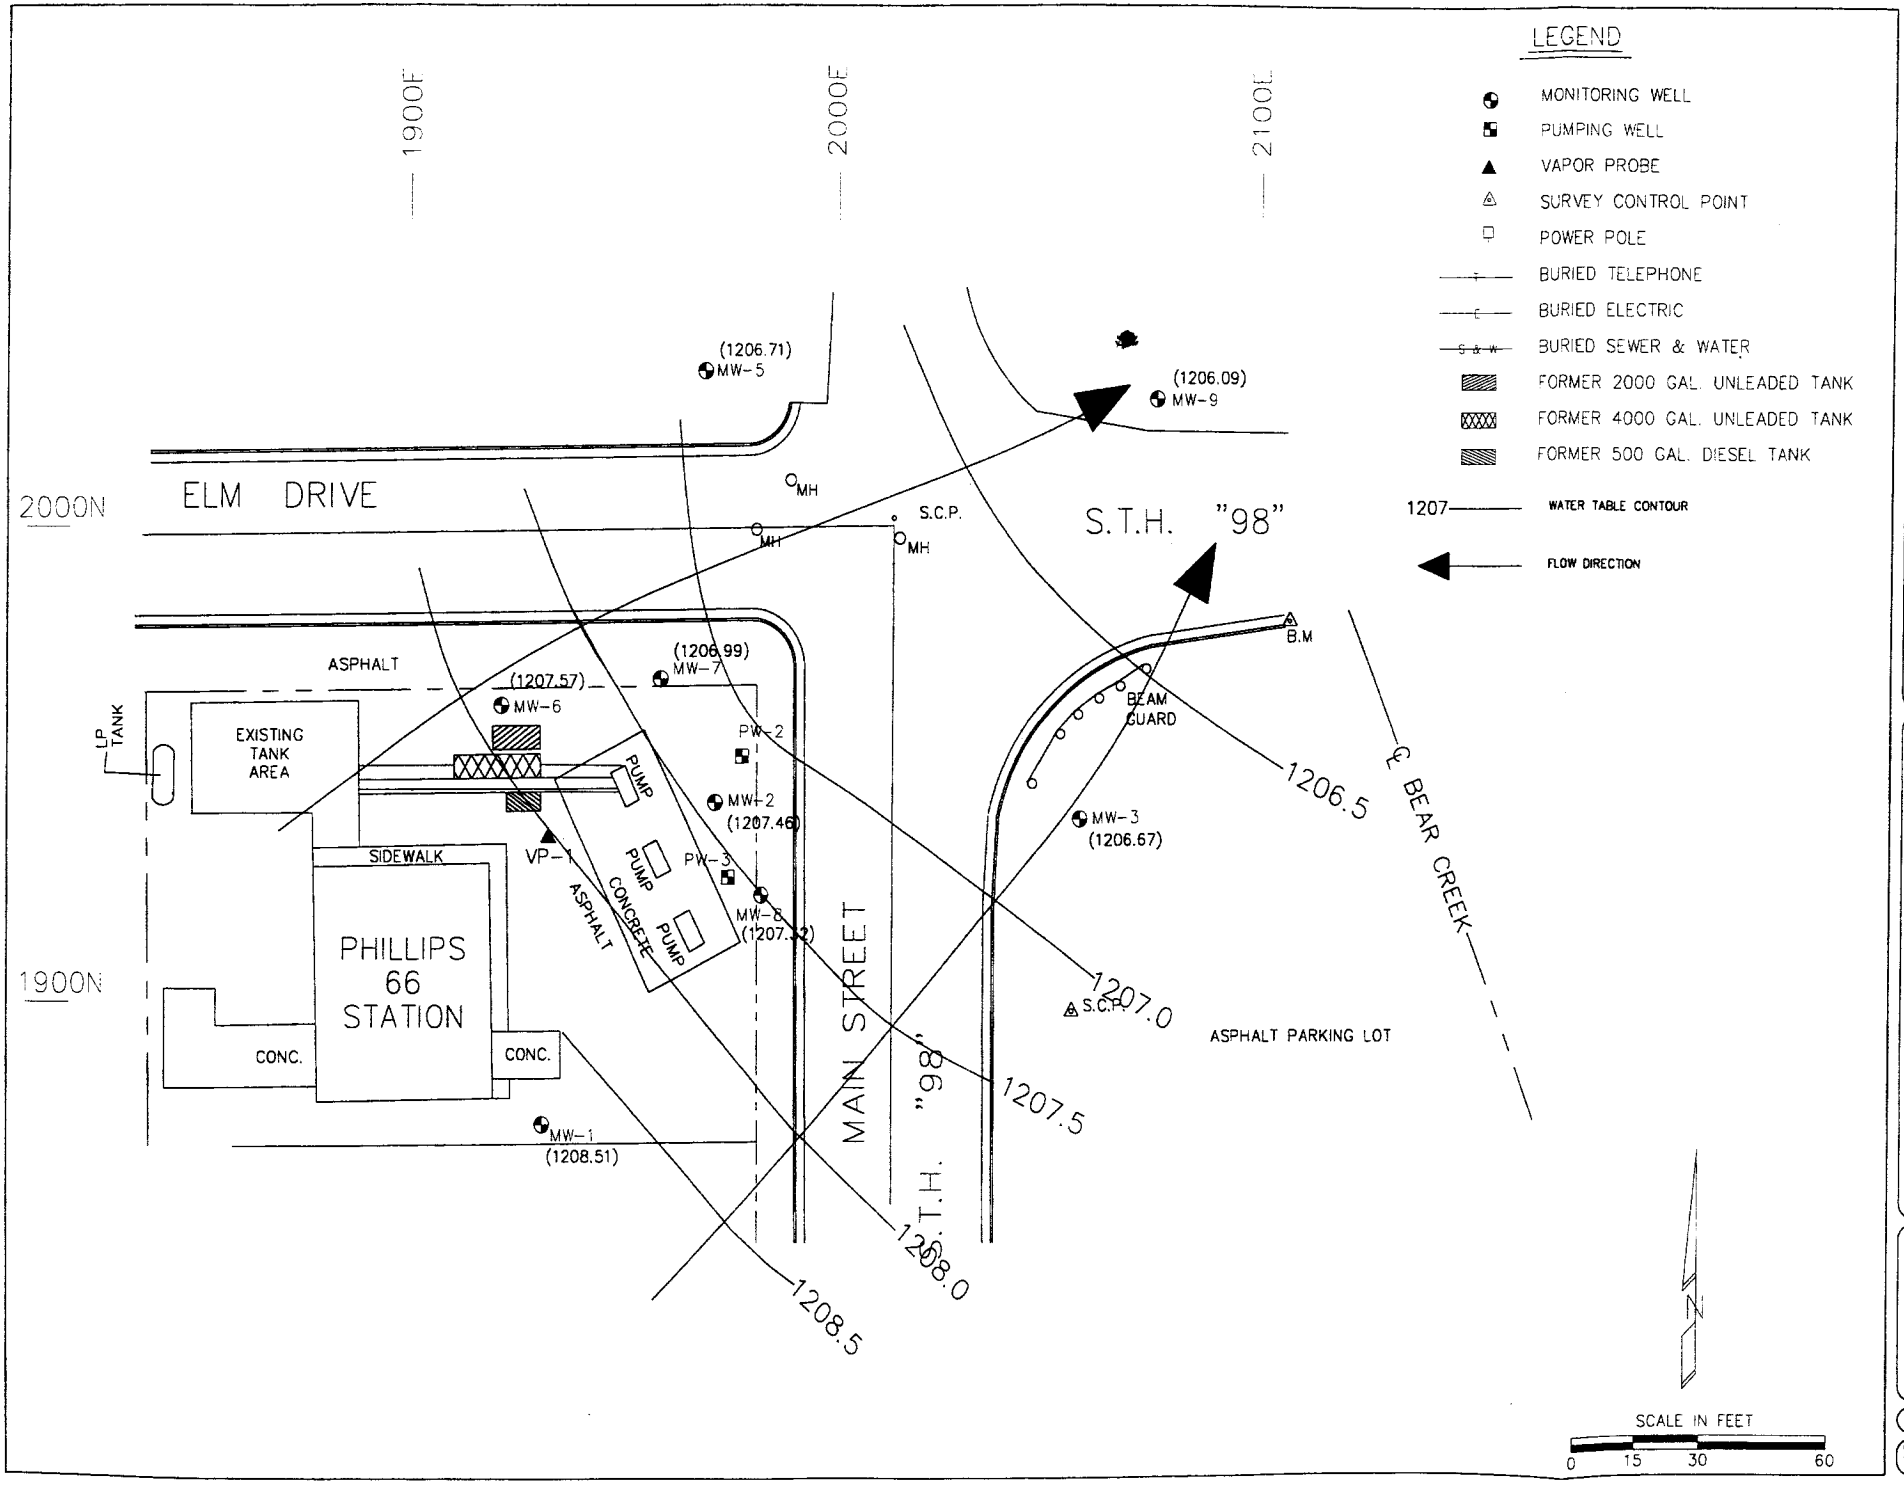

CENTRAL WISCONSIN ENGINEERS AND ARCHITECTS, INC.
5707 SCHOFIELD AVENUE WESTON, WISCONSIN 54476
PHONE: (715) 359-9400 FAX: (715) 355-4199

PROJECT:

WATER TABLE CONTOUR MAP
FOR 10/07/99
LOYAL 66 SERVICE STATION
LOYAL, WISCONSIN

DRAWN BY: H.S.
CHECKED BY: P.S.
APPROVED BY:
DATE: 05/00
PROJECT NO: 13090070
DNR NO: 03-10-000388

FIGURE: 7

CAD FILE:

Table 3
Post-Remediation Groundwater Monitoring Data, Loyal 66 Service Station, Loyal, WI
WDNR Project No: 03-10-000388

ABBREVIATIONS, SYMBOLS, & NOTES

PAL: Preventive Action Limit
ES: Enforcement Standard
PQL: Practical Quantitation Limit
GRO: Gasoline Range Organics
DRO: Diesel Range Organics
-: Regulatory limit not established.
--: Not Analyzed N: Not Detected

<"n" denotes not detected where "n" is the detection limit greater than listed under PQL.
V = Full VOC scan performed; no other compounds included in the method were detected.
[1] Listed values are commonly reported minimum PQLs.

Indicates concentration exceeds NR 140 Preventive Action Limit.
Indicates concentration exceeds NR 140 Enforcement Standard.

Well I.D. MW-1

PVC Elevation	1214.08															
Ground Elevation	1214.70	Sample Date			1/5/93	4/12/93	7/20/93	10/6/93	1/6/94	6/8/94	10/5/94	12/30/94	3/31/95	7/12/95	10/16/95	1/16/96
Screen Top Elevation	1208.7	Depth to Water (ft)			5.10	3.81	4.52	4.11	--	5.34	5.82	6.56	5.07	6.51	5.87	6.68
Point Elevation	1198.7	Water Elevation (ft)			1208.98	1210.27	1209.56	1209.97		1208.74	1208.26	1207.52	1209.01	1207.57	1208.21	1207.40
		Notes:														
ORGANICS		PAL	ES	PQL[1]												
GRO	(µg/L)	-	-	50	<10	<50	<50	<50	--	<50	--	<50	--	N	N	N
DRO	(µg/L)	-	-	100	--	--	--	--	--	--	--	--	--	--	--	--
Benzene	(µg/L)	0.5	5.0	1	N	N	N	N	--	N	--	N	--	N	N	N
Ethylbenzene	(µg/L)	140	700	1	N	N	N	N	--	N	--	N	--	N	N	N
Toluene	(µg/L)	200	1000	1	N	N	N	N	--	N	--	N	--	N	N	N
o-Xylene/Styrene	(µg/L)	-	-	1	N	N	N	N	--	N	--	N	--	N	N	N
m- & p- Xylenes	(µg/L)	-	-	1	N	N	N	N	--	N	--	N	--	N	N	N
Total Xylenes	(µg/L)	1000	10000	2	N	N	N	N	--	N	--	N	--	N	N	N
Methyl-t-butyl ether	(µg/L)	12	60	3	<10	N	N	N	--	N	--	N	--	N	N	N
1,2,4-Trimethylbenzene	(µg/L)	-	-	3	N	N	N	N	--	N	--	N	--	N	N	N
1,3,5-Trimethylbenzene	(µg/L)	-	-	1	N	N	N	N	--	N	--	N	--	N	N	N
Total Trimethylbenzene	(µg/L)	96	480	4	N	N	N	N	--	N	--	N	--	N	N	N
FIELD MEASUREMENTS																
Temperature	(°C)	-	-	-	--	--	--	--	--	--	--	--	--	--	--	--
Dissolved Oxygen	(mg/L)	-	-	-	--	--	--	--	--	--	--	--	--	--	--	--
pH	(S.U.)	-	-	-	--	--	--	--	--	--	--	--	--	--	--	--
Conductivity	(µmho/cm)	-	-	-	--	--	--	--	--	--	--	--	--	--	--	--

Table 3
Post-Remediation Groundwater Monitoring Data, Loyal 66 Service Station, Loyal, WI
WDNR Project No: 03-10-000388

ABBREVIATIONS, SYMBOLS, & NOTES

PAL: Preventive Action Limit
ES: Enforcement Standard
PQL: Practical Quantitation Limit
GRO: Gasoline Range Organics
DRO: Diesel Range Organics
-: Regulatory limit not established.
--: Not Analyzed N: Not Detected

<"n" denotes not detected where "n" is the detection limit greater than listed under PQL.
V = Full VOC scan performed; no other compounds included in the method were detected.
[1] Listed values are commonly reported minimum PQLs.

Indicates concentration exceeds NR 140 Preventive Action Limit.
Indicates concentration exceeds NR 140 Enforcement Standard.

Well I.D. MW-1

PVC Elevation	1214.08																
Ground Elevation	1214.70	Sample Date			4/9/96	7/12/96	10/14/96	1/2/97	4/1/97	7/21/97	10/20/97	4/8/98	10/22/98	5/3/99	10/7/99	10/25/00	1/25/01
Screen Top Elevation	1208.7	Depth to Water (ft)			5.23	5.28	6.01	5.48	4.22	5.59	4.67	4.72	5.94	5.06	1.57	--	--
Point Elevation	1198.7	Water Elevation (ft)			1208.85	1208.80	1208.07	1208.60	1209.86	1208.49	1209.41	1209.36	1208.14	1209.02	1212.51		
		Notes:															
ORGANICS		PAL	ES	PQL[1]													
GRO	(µg/L)	-	-	50	--	--	44	--	N	N	N	--	N	N	N	--	--
DRO	(µg/L)	-	-	100	--	--	--	--	--	--	--	--	--	--	--	--	--
Benzene	(µg/L)	0.5	5.0	1	--	--	N	--	N	N	N	--	N	N	N	--	--
Ethylbenzene	(µg/L)	140	700	1	--	--	N	--	N	N	N	--	N	N	N	--	--
Toluene	(µg/L)	200	1000	1	--	--	N	--	N	N	N	--	N	N	N	--	--
o-Xylene/Styrene	(µg/L)	-	-	1	--	--	N	--	N	N	N	--	N	N	N	--	--
m- & p- Xylenes	(µg/L)	-	-	1	--	--	N	--	N	N	N	--	N	N	N	--	--
Total Xylenes	(µg/L)	1000	10000	2	--	--	N	--	N	N	N	--	N	N	N	--	--
Methyl-t-butyl ether	(µg/L)	12	60	3	--	--	N	--	N	N	N	--	N	N	N	--	--
1,2,4-Trimethylbenzene	(µg/L)	-	-	3	--	--	N	--	N	N	N	--	N	N	N	--	--
1,3,5-Trimethylbenzene	(µg/L)	-	-	1	--	--	N	--	N	N	N	--	N	N	N	--	--
Total Trimethylbenzene	(µg/L)	96	480	4	--	--	N	--	N	N	N	--	N	N	N	--	--
FIELD MEASUREMENTS																	
Temperature	(°C)	-	-	-	--	--	--	--	--	--	--	--	--	--	13.6	--	--
Dissolved Oxygen	(mg/L)	-	-	-	--	--	--	--	--	--	--	--	--	--	0.8	--	--
pH	(S.U.)	-	-	-	--	--	--	--	--	--	--	--	--	--	6.41	--	--
Conductivity	(µmho/cm)	-	-	-	--	--	--	--	--	--	--	--	--	--	233	--	--

Table 3
Post-Remediation Groundwater Monitoring Data, Loyal 66 Service Station, Loyal, WI
WDNR Project No: 03-10-000388

ABBREVIATIONS, SYMBOLS, & NOTES

PAL: Preventive Action Limit
ES: Enforcement Standard
PQL: Practical Quantitation Limit
GRO: Gasoline Range Organics
DRO: Diesel Range Organics
-: Regulatory limit not established.
--: Not Analyzed N: Not Detected

<"n" denotes not detected where "n" is the detection limit greater than listed under PQL.
V = Full VOC scan performed; no other compounds included in the method were detected.
[1] Listed values are commonly reported minimum PQLs.

Indicates concentration exceeds NR 140 Preventive Action Limit.
Indicates concentration exceeds NR 140 Enforcement Standard.

Well I.D. MW-2

PVC Elevation	1213.26															
Ground Elevation	1213.62	Sample Date			1/5/93	4/12/93	7/20/93	10/6/93	1/6/94	6/8/94	10/5/94	12/30/94	3/31/95	7/12/95	10/16/95	1/16/96
Screen Top Elevation	1207.1	Depth to Water (ft)			5.42	4.52	8.26	4.30	8.74	7.55	8.11	10.52	5.63	9.44	8.70	--
Point Elevation	1197.1	Water Elevation (ft)			1207.83	1208.73	1205.00	1208.96	1204.52	1205.71	1205.15	1202.74	1207.63	1203.82	1204.56	
PVC Ele. Before 7/20/93	1213.25	Notes:														
ORGANICS		PAL	ES	PQL[1]												
GRO	(µg/L)	-	-	50	3,090	5,470	19,200	13,800	18,300	--	--	--	--	--	--	--
DRO	(µg/L)	-	-	100	--	--	--	--	--	--	--	--	--	--	--	--
Benzene	(µg/L)	0.5	5.0	1	**45**	**122**	**671**	**79**	**949**	--	--	--	--	--	--	--
Ethylbenzene	(µg/L)	140	700	1	21	**190**	**842**	**480**	**669**	--	--	--	--	--	--	--
Toluene	(µg/L)	200	1000	1	25	**364**	**1,420**	**443**	**1,210**	--	--	--	--	--	--	--
o-Xylene/Styrene	(µg/L)	-	-	1	41	216	782	819	600	--	--	--	--	--	--	--
m- & p- Xylenes	(µg/L)	-	-	1	97	710	2,080	2,390	2,080	--	--	--	--	--	--	--
Total Xylenes	(µg/L)	1000	10000	2	138	926	**2,862**	**3,209**	**2,680**	--	--	--	--	--	--	--
Methyl-t-butyl ether	(µg/L)	12	60	3	<10	**104**	**462**	<30	<30	--	--	--	--	--	--	--
1,2,4-Trimethylbenzene	(µg/L)	-	-	3	77	284	829	1,150	990	--	--	--	--	--	--	--
1,3,5-Trimethylbenzene	(µg/L)	-	-	1	49	95	246	383	295	--	--	--	--	--	--	--
Total Trimethylbenzene	(µg/L)	96	480	4	**126**	**379**	**1,075**	**1,533**	**1,285**	--	--	--	--	--	--	--
FIELD MEASUREMENTS																
Temperature	(°C)	-	-	-	--	--	--	--	--	--	--	--	--	--	--	--
Dissolved Oxygen	(mg/L)	-	-	-	--	--	--	--	--	--	--	--	--	--	--	--
pH	(S.U.)	-	-	-	--	--	--	--	--	--	--	--	--	--	--	--
Conductivity	(µmho/cm)	-	-	-	--	--	--	--	--	--	--	--	--	--	--	--

Table 3
Post-Remediation Groundwater Monitoring Data, Loyal 66 Service Station, Loyal, WI
WDNR Project No: 03-10-000388

ABBREVIATIONS, SYMBOLS, & NOTES

PAL: Preventive Action Limit
ES: Enforcement Standard
PQL: Practical Quantitation Limit
GRO: Gasoline Range Organics
DRO: Diesel Range Organics
-: Regulatory limit not established.
--: Not Analyzed N: Not Detected

<"n" denotes not detected where "n" is the detection limit greater than listed under PQL.
V = Full VOC scan performed; no other compounds included in the method were detected.
[1] Listed values are commonly reported minimum PQLs.

Indicates concentration exceeds NR 140 Preventive Action Limit.
Indicates concentration exceeds NR 140 Enforcement Standard.

Well I.D. MW-2

PVC Elevation	1213.26															
Ground Elevation	1213.62	Sample Date			4/9/96	7/12/96	10/14/96	1/2/97	4/1/97	7/21/97	10/20/97	4/8/98	10/22/98	5/3/99	10/7/99	10/25/00	1/25/01
Screen Top Elevation	1207.1	Depth to Water (ft)			6.30	3.98	7.97	6.72	4.96	8.26	7.90	4.28	--	4.03	5.80	6.22	6.40
Point Elevation	1197.1	Water Elevation (ft)			1206.96	1209.28	1205.29	1206.54	1208.30	1205.00	1205.36	1208.98		1209.23	1207.46	1207.04	1206.86
PVC Ele. Before 7/20/93	1213.25	Notes:															
ORGANICS		PAL	ES	PQL[1]													
GRO	(µg/L)	-	-	50	--	550	12,000	8,500	6,500	1,300	2,700	1,300	2,460	--	317	900	1560
DRO	(µg/L)	-	-	100	--	--	--	--	--	--	--	--	--	--	--	--	--
Benzene	(µg/L)	0.5	5.0	1	--	N	**180**	**150**	**16**	**42**	**130**	**6.6**	**78**	**9.4**	**4.6**	**41**	**51**
Ethylbenzene	(µg/L)	140	700	1	--	2.1	**180**	140	32	5.2	61	9.1	59	33	2.8	13	19
Toluene	(µg/L)	200	1000	1	--	0.70	100	100	19	37	110	5.5	127	14	1.6	18	19
o-Xylene/Styrene	(µg/L)	-	-	1	--	1.4	220	200	51	45	160	17	161	63	6.3	--	--
m- & p- Xylenes	(µg/L)	-	-	1	--	2.3	660	640	110	76	380	25	364	148	7.1	--	--
Total Xylenes	(µg/L)	1000	10000	2	--	3.7	880	840	161	121	540	42	525	211	13	79	94
Methyl-t-butyl ether	(µg/L)	12	60	3	--	N	N	N	N	N	N	N	N	N	N	**12**	<1.8
1,2,4-Trimethylbenzene	(µg/L)	-	-	3	--	12	430	450	130	33	120	19	159	100	9.9	37	47
1,3,5-Trimethylbenzene	(µg/L)	-	-	1	--	5.2	160	180	72	21	57	10	69	64	N	12	17
Total Trimethylbenzene	(µg/L)	96	480	4	--	17	**590**	**630**	**202**	54	**177**	29	**228**	**164**	9.9	49	64
FIELD MEASUREMENTS																	
Temperature	(°C)	-	-	-	--	--	--	--	--	--	--	--	--	--	15.0	14.5	7.2
Dissolved Oxygen	(mg/L)	-	-	-	--	--	--	--	--	--	--	--	--	--	0.1	0.0	0.1
pH	(S.U.)	-	-	-	--	--	--	--	--	--	--	--	--	--	6.63	6.44	6.04
Conductivity	(µmho/cm)	-	-	-	--	--	--	--	--	--	--	--	--	--	690	1050	1050

Table 3
Post-Remediation Groundwater Monitoring Data, Loyal 66 Service Station, Loyal, WI
WDNR Project No: 03-10-000388

ABBREVIATIONS, SYMBOLS, & NOTES

PAL: Preventive Action Limit
ES: Enforcement Standard
PQL: Practical Quantitation Limit
GRO: Gasoline Range Organics
DRO: Diesel Range Organics
-: Regulatory limit not established.
--: Not Analyzed N: Not Detected

<"n" denotes not detected where "n" is the detection limit greater than listed under PQL.
V = Full VOC scan performed; no other compounds included in the method were detected.
[1] Listed values are commonly reported minimum PQLs.

Indicates concentration exceeds NR 140 Preventive Action Limit.
Indicates concentration exceeds NR 140 Enforcement Standard.

Well I.D. MW-3

PVC Elevation	1212.55															
Ground Elevation	1213.16	Sample Date			1/5/93	4/12/93	7/20/93	10/6/93	1/6/94	6/8/94	10/5/94	12/30/94	3/31/95	7/12/95	10/16/95	1/16/96
Screen Top Elevation	1204.3	Depth to Water (ft)			--	--	--	--	--	6.06	6.37	7.33	5.51	7.06	6.73	7.36
Point Elevation	1194.3	Water Elevation (ft)								1206.49	1206.18	1205.22	1207.04	1205.49	1205.82	1205.19
PVC Ele. Before 5/5/93	1212.81	Notes:														
ORGANICS		PAL	ES	PQL[1]												
GRO	(µg/L)	-	-	50	--	--	--	--	--	<50	--	<50	--	N	N	N
DRO	(µg/L)	-	-	100	--	--	--	--	--	--	--	--	--	--	--	--
Benzene	(µg/L)	0.5	5.0	1	--	--	--	--	--	N	--	N	--	N	N	N
Ethylbenzene	(µg/L)	140	700	1	--	--	--	--	--	N	--	N	--	N	N	N
Toluene	(µg/L)	200	1000	1	--	--	--	--	--	N	--	N	--	0.70	N	N
o-Xylene/Styrene	(µg/L)	-	-	1	--	--	--	--	--	N	--	N	--	N	N	N
m- & p- Xylenes	(µg/L)	-	-	1	--	--	--	--	--	N	--	N	--	N	N	N
Total Xylenes	(µg/L)	1000	10000	2	--	--	--	--	--	N	--	N	--	N	N	N
Methyl-t-butyl ether	(µg/L)	12	60	3	--	--	--	--	--	N	--	N	--	N	N	N
1,2,4-Trimethylbenzene	(µg/L)	-	-	3	--	--	--	--	--	N	--	N	--	N	N	N
1,3,5-Trimethylbenzene	(µg/L)	-	-	1	--	--	--	--	--	N	--	N	--	N	N	N
Total Trimethylbenzene	(µg/L)	96	480	4	--	--	--	--	--	N	--	N	--	N	N	N
FIELD MEASUREMENTS																
Temperature	(°C)	-	-	-	--	--	--	--	--	--	--	--	--	--	--	--
Dissolved Oxygen	(mg/L)	-	-	-	--	--	--	--	--	--	--	--	--	--	--	--
pH	(S.U.)	-	-	-	--	--	--	--	--	--	--	--	--	--	--	--
Conductivity	(µmho/cm)	-	-	-	--	--	--	--	--	--	--	--	--	--	--	--

Table 3
Post-Remediation Groundwater Monitoring Data, Loyal 66 Service Station, Loyal, WI
WDNR Project No: 03-10-000388

ABBREVIATIONS, SYMBOLS, & NOTES

PAL: Preventive Action Limit
ES: Enforcement Standard
PQL: Practical Quantitation Limit
GRO: Gasoline Range Organics
DRO: Diesel Range Organics
-: Regulatory limit not established.
—: Not Analyzed N: Not Detected

<"n" denotes not detected where "n" is the detection limit greater than listed under PQL.
V = Full VOC scan performed; no other compounds included in the method were detected.
[1] Listed values are commonly reported minimum PQLs.

Indicates concentration exceeds NR 140 Preventive Action Limit.
Indicates concentration exceeds NR 140 Enforcement Standard.

Well I.D. MW-3

PVC Elevation	1212.55																
Ground Elevation	1213.16	Sample Date			4/9/96	7/12/96	10/14/96	1/2/97	4/1/97	7/21/97	10/20/97	4/8/98	10/22/98	5/3/99	10/7/99	10/25/00	1/25/01
Screen Top Elevation	1204.3	Depth to Water (ft)			6.53	--	6.72	--	5.71	6.72	--	5.91	6.33	6.04	5.88	--	--
Point Elevation	1194.3	Water Elevation (ft)			1206.02		1205.83		1206.84	1205.83		1206.64	1206.22	1206.51	1206.67		
PVC Ele. Before 5/5/93	1212.81	Notes:															
ORGANICS		PAL	ES	PQL[1]													
GRO	(µg/L)	-	-	50	--	--	27	--	N	N	--	--	N	--	N	--	--
DRO	(µg/L)	-	-	100	--	--	--	--	--	--	--	--	--	--	--	--	--
Benzene	(µg/L)	0.5	5.0	1	--	--	N	--	N	N	--	--	N	N	N	--	--
Ethylbenzene	(µg/L)	140	700	1	--	--	N	--	N	N	--	--	N	N	N	--	--
Toluene	(µg/L)	200	1000	1	--	--	N	--	N	N	--	--	N	N	N	--	--
o-Xylene/Styrene	(µg/L)	-	-	1	--	--	N	--	N	N	--	--	N	N	N	--	--
m- & p- Xylenes	(µg/L)	-	-	1	--	--	N	--	N	N	--	--	N	N	N	--	--
Total Xylenes	(µg/L)	1000	10000	2	--	--	N	--	N	N	--	--	N	N	N	--	--
Methyl-t-butyl ether	(µg/L)	12	60	3	--	--	N	--	N	N	--	--	N	N	N	--	--
1,2,4-Trimethylbenzene	(µg/L)	-	-	3	--	--	N	--	N	N	--	--	N	N	N	--	--
1,3,5-Trimethylbenzene	(µg/L)	-	-	1	--	--	N	--	N	N	--	--	N	N	N	--	--
Total Trimethylbenzene	(µg/L)	96	480	4	--	--	N	--	N	N	--	--	N	N	N	--	--
FIELD MEASUREMENTS																	
Temperature	(°C)	-	-	-	--	--	--	--	--	--	--	--	--	--	14.5	--	--
Dissolved Oxygen	(mg/L)	-	-	-	--	--	--	--	--	--	--	--	--	--	0.2	--	--
pH	(S.U.)	-	-	-	--	--	--	--	--	--	--	--	--	--	6.61	--	--
Conductivity	(µmho/cm)	-	-	-	--	--	--	--	--	--	--	--	--	--	780	--	--

Table 3
Post-Remediation Groundwater Monitoring Data, Loyal 66 Service Station, Loyal, WI
WDNR Project No: 03-10-000388

ABBREVIATIONS, SYMBOLS, & NOTES

PAL: Preventive Action Limit
ES: Enforcement Standard
PQL: Practical Quantitation Limit
GRO: Gasoline Range Organics
DRO: Diesel Range Organics
-: Regulatory limit not established.
--: Not Analyzed N: Not Detected

<"n" denotes not detected where "n" is the detection limit greater than listed under PQL.
V = Full VOC scan performed; no other compounds included in the method were detected.
[1] Listed values are commonly reported minimum PQLs.

Indicates concentration exceeds NR 140 Preventive Action Limit.
Indicates concentration exceeds NR 140 Enforcement Standard.

Well I.D. MW-5

PVC Elevation	1212.31															
Ground Elevation	1212.70	Sample Date			1/5/93	4/12/93	7/20/93	10/6/93	1/6/94	6/8/94	10/5/94	12/30/94	3/31/95	7/12/95	10/16/95	1/16/96
Screen Top Elevation	1207.7	Depth to Water (ft)			5.26	5.02	5.52	4.64	6.24	5.73	6.03	6.99	5.14	6.79	6.42	6.94
Point Elevation	1197.7	Water Elevation (ft)			1207.05	1207.29	1206.79	1207.67	1206.07	1206.58	1206.28	1205.32	1207.17	1205.52	1205.89	1205.37
		Notes:														
ORGANICS		PAL	ES	PQL[1]												
GRO	(µg/L)	-	-	50	<10	<50	N	N	N	N	N	N	N	N	N	N
DRO	(µg/L)	-	-	100	--	--	--	--	--	--	--	--	--	--	--	--
Benzene	(µg/L)	0.5	5.0	1	N	N	8.5	1.6	N	N	1.5	N	N	N	0.50	N
Ethylbenzene	(µg/L)	140	700	1	N	N	N	N	N	N	N	N	N	N	N	N
Toluene	(µg/L)	200	1000	1	N	N	N	N	N	N	N	N	N	N	0.90	N
o-Xylene/Styrene	(µg/L)	-	-	1	N	N	N	N	N	N	N	N	N	N	N	N
m- & p- Xylenes	(µg/L)	-	-	1	N	N	N	N	N	N	N	N	N	N	N	N
Total Xylenes	(µg/L)	1000	10000	2	--	N	N	N	N	N	N	N	N	N	N	N
Methyl-t-butyl ether	(µg/L)	12	60	3	<10	N	N	N	N	N	N	N	N	N	N	N
1,2,4-Trimethylbenzene	(µg/L)	-	-	3	N	N	N	N	N	N	N	N	N	N	N	N
1,3,5-Trimethylbenzene	(µg/L)	-	-	1	N	N	N	N	N	N	N	N	N	N	N	N
Total Trimethylbenzene	(µg/L)	96	480	4	N	N	N	N	N	N	N	N	N	N	N	N
FIELD MEASUREMENTS																
Temperature	(°C)	-	-	-	--	--	--	--	--	--	--	--	--	--	--	--
Dissolved Oxygen	(mg/L)	-	-	-	--	--	--	--	--	--	--	--	--	--	--	--
pH	(S.U.)	-	-	-	--	--	--	--	--	--	--	--	--	--	--	--
Conductivity	(µmho/cm)	-	-	-	--	--	--	--	--	--	--	--	--	--	--	--

Table 3
Post-Remediation Groundwater Monitoring Data, Loyal 66 Service Station, Loyal, WI
WDNR Project No: 03-10-000388

ABBREVIATIONS, SYMBOLS, & NOTES

PAL: Preventive Action Limit
ES: Enforcement Standard
PQL: Practical Quantitation Limit
GRO: Gasoline Range Organics
DRO: Diesel Range Organics
-: Regulatory limit not established.
--: Not Analyzed N: Not Detected

<"n" denotes not detected where "n" is the detection limit greater than listed under PQL.
V = Full VOC scan performed; no other compounds included in the method were detected.
[1] Listed values are commonly reported minimum PQLs.

Indicates concentration exceeds NR 140 Preventive Action Limit.
Indicates concentration exceeds NR 140 Enforcement Standard.

Well I.D. MW-5

PVC Elevation	1212.31															
Ground Elevation	1212.70	Sample Date			4/9/96	7/12/96	10/14/96	1/2/97	4/1/97	7/21/97	10/20/97	4/8/98	10/22/98	5/3/99	10/7/99	10/25/00	1/25/01
Screen Top Elevation	1207.7	Depth to Water (ft)			6.02	6.13	6.41	5.57	5.19	6.30	5.54	5.38	4.86	5.47	5.60	5.76	--
Point Elevation	1197.7	Water Elevation (ft)			1206.29	1206.18	1205.90	1206.74	1207.12	1206.01	1206.77	1206.93	1207.45	1206.84	1206.71	1206.55	
		Notes:															
ORGANICS		PAL	ES	PQL[1]													
GRO	(µg/L)	-	-	50	N	N	N	N	N	N	N	52	N	--	30	<17	--
DRO	(µg/L)	-	-	100	--	--	--	--	--	--	--	--	--	--	--	--	--
Benzene	(µg/L)	0.5	5.0	1	N	**0.50**	**2.6**	**1.6**	**1.1**	N	N	**4.4**	**0.91**	N	**1.2**	<0.5	--
Ethylbenzene	(µg/L)	140	700	1	N	N	N	N	N	N	N	N	N	N	N	<0.6	--
Toluene	(µg/L)	200	1000	1	N	N	N	N	N	N	N	N	N	N	N	<0.6	--
o-Xylene/Styrene	(µg/L)	-	-	1	N	N	N	N	N	N	N	N	N	N	N	--	--
m- & p- Xylenes	(µg/L)	-	-	1	N	N	N	N	N	N	N	N	N	N	N	--	--
Total Xylenes	(µg/L)	1000	10000	2	N	N	N	N	N	N	N	N	N	N	N	<1.7	--
Methyl-t-butyl ether	(µg/L)	12	60	3	N	N	N	N	N	N	N	N	N	N	N	<0.92	--
1,2,4-Trimethylbenzene	(µg/L)	-	-	3	N	N	N	N	N	N	N	0.30	N	N	N	<1.7	--
1,3,5-Trimethylbenzene	(µg/L)	-	-	1	N	N	N	N	N	N	N	N	N	N	N	<0.9	--
Total Trimethylbenzene	(µg/L)	96	480	4	N	N	N	N	N	N	N	0.30	N	N	N	<2.6	--
FIELD MEASUREMENTS																	
Temperature	(°C)	-	-	-	--	--	--	--	--	--	--	--	--	--	15.3	14.7	--
Dissolved Oxygen	(mg/L)	-	-	-	--	--	--	--	--	--	--	--	--	--	3.8	3.5	--
pH	(S.U.)	-	-	-	--	--	--	--	--	--	--	--	--	--	6.73	6.80	--
Conductivity	(µmho/cm)	-	-	-	--	--	--	--	--	--	--	--	--	--	439	420	--

Table 3
Post-Remediation Groundwater Monitoring Data, Loyal 66 Service Station, Loyal, WI
WDNR Project No: 03-10-000388

ABBREVIATIONS, SYMBOLS, & NOTES

PAL: Preventive Action Limit
ES: Enforcement Standard
PQL: Practical Quantitation Limit
GRO: Gasoline Range Organics
DRO: Diesel Range Organics
-: Regulatory limit not established.
--: Not Analyzed N: Not Detected

<"n" denotes not detected where "n" is the detection limit greater than listed under PQL.
V = Full VOC scan performed; no other compounds included in the method were detected.
[1] Listed values are commonly reported minimum PQLs.

Indicates concentration exceeds NR 140 Preventive Action Limit.
Indicates concentration exceeds NR 140 Enforcement Standard.

Well I.D. MW-6

PVC Elevation	1212.39															
Ground Elevation	1213.90	Sample Date			1/5/93	4/12/93	7/20/93	10/6/93	1/6/94	6/8/94	10/5/94	12/30/94	3/31/95	7/12/95	10/16/95	1/16/96
Screen Top Elevation	1208.9	Depth to Water (ft)			4.74	2.96	4.76	5.62	5.56	5.02	5.42	6.23	5.29	6.09	5.42	6.66
Point Elevation	1198.9	Water Elevation (ft)			1207.65	1209.43	1207.63	1206.77	1206.83	1207.37	1206.97	1206.16	1207.10	1206.30	1206.97	1205.73
		Notes:														
ORGANICS		PAL	ES	PQL[1]												
GRO	(µg/L)	-	-	50	<10	640	N	N	N	52	N	N	N	N	N	N
DRO	(µg/L)	-	-	100	--	--	--	--	--	--	--	--	--	--	--	--
Benzene	(µg/L)	0.5	5.0	1	N	**22**	**15**	**22**	N	**17**	**3.8**	N	N	**1.5**	**2.6**	N
Ethylbenzene	(µg/L)	140	700	1	N	N	N	N	N	N	N	N	N	N	N	N
Toluene	(µg/L)	200	1000	1	N	N	N	N	N	N	N	N	N	0.80	0.80	N
o-Xylene/Styrene	(µg/L)	-	-	1	N	2.1	N	N	N	1.6	N	N	N	N	N	N
m- & p- Xylenes	(µg/L)	-	-	1	N	N	1.3	N	N	N	N	N	N	N	N	N
Total Xylenes	(µg/L)	1000	10000	2	--	2.1	1.3	N	N	1.6	N	N	N	N	N	N
Methyl-t-butyl ether	(µg/L)	12	60	3	<10	N	N	N	N	N	N	N	N	N	N	N
1,2,4-Trimethylbenzene	(µg/L)	-	-	3	N	1.3	N	N	N	N	N	N	N	N	N	N
1,3,5-Trimethylbenzene	(µg/L)	-	-	1	N	N	N	N	N	N	N	N	N	N	N	N
Total Trimethylbenzene	(µg/L)	96	480	4	N	1.3	N	N	N	N	N	N	N	N	N	N
FIELD MEASUREMENTS																
Temperature	(°C)	-	-	-	--	--	--	--	--	--	--	--	--	--	--	--
Dissolved Oxygen	(mg/L)	-	-	-	--	--	--	--	--	--	--	--	--	--	--	--
pH	(S.U.)	-	-	-	--	--	--	--	--	--	--	--	--	--	--	--
Conductivity	(µmho/cm)	-	-	-	--	--	--	--	--	--	--	--	--	--	--	--

Table 3
Post-Remediation Groundwater Monitoring Data, Loyal 66 Service Station, Loyal, WI
WDNR Project No: 03-10-000388

ABBREVIATIONS, SYMBOLS, & NOTES

PAL: Preventive Action Limit
ES: Enforcement Standard
PQL: Practical Quantitation Limit
GRO: Gasoline Range Organics
DRO: Diesel Range Organics
-: Regulatory limit not established.
--: Not Analyzed N: Not Detected

<"n" denotes not detected where "n" is the detection limit greater than listed under PQL.
V = Full VOC scan performed; no other compounds included in the method were detected.
[1] Listed values are commonly reported minimum PQLs.

Indicates concentration exceeds NR 140 Preventive Action Limit.
Indicates concentration exceeds NR 140 Enforcement Standard.

Well I.D. MW-6

PVC Elevation	1212.39															
Ground Elevation	1213.90	Sample Date			4/9/96	7/12/96	10/14/96	1/2/97	4/1/97	7/21/97	10/20/97	4/8/98	10/22/98	5/3/99	10/7/99	10/25/00	1/25/01
Screen Top Elevation	1208.9	Depth to Water (ft)			5.13	4.62	5.93	5.27	3.79	5.34	4.65	4.07	5.94	4.77	4.82	--	6.14
Point Elevation	1198.9	Water Elevation (ft)			1207.26	1207.77	1206.46	1207.12	1208.60	1207.05	1207.74	1208.32	1206.45	1207.62	1207.57		1206.25
		Notes:															
ORGANICS		PAL	ES	PQL[1]													
GRO	(µg/L)	-	-	50	N	N	32	N	N	N	N	N	N	--	56	--	<5.9
DRO	(µg/L)	-	-	100	--	--	--	--	--	--	--	--	--	--	--	--	--
Benzene	(µg/L)	0.5	5.0	1	N	N	**1.2**	N	**0.7**	N	N	N	N	N	**1.8**	--	<0.21
Ethylbenzene	(µg/L)	140	700	1	N	N	N	0.30	N	N	N	N	N	N	N	--	<0.23
Toluene	(µg/L)	200	1000	1	N	N	N	0.50	N	N	N	N	14	N	4.6	--	<0.22
o-Xylene/Styrene	(µg/L)	-	-	1	N	N	N	0.60	N	N	N	N	N	N	N	--	--
m- & p- Xylenes	(µg/L)	-	-	1	N	N	N	1.4	N	N	N	N	N	N	N	--	--
Total Xylenes	(µg/L)	1000	10000	2	N	N	N	2.0	N	N	N	N	N	N	N	--	<0.44
Methyl-t-butyl ether	(µg/L)	12	60	3	N	N	N	N	N	N	N	N	N	N	N	--	<0.091
1,2,4-Trimethylbenzene	(µg/L)	-	-	3	N	N	N	1.6	N	N	N	N	N	N	N	--	<0.23
1,3,5-Trimethylbenzene	(µg/L)	-	-	1	N	N	N	0.40	N	N	N	N	N	N	N	--	<0.21
Total Trimethylbenzene	(µg/L)	96	480	4	N	N	N	2.0	N	N	N	N	N	N	N	--	<0.44
FIELD MEASUREMENTS																	
Temperature	(°C)	-	-	-	--	--	--	--	--	--	--	--	--	--	16.8	--	8.6
Dissolved Oxygen	(mg/L)	-	-	-	--	--	--	--	--	--	--	--	--	--	0.1	--	0.1
pH	(S.U.)	-	-	-	--	--	--	--	--	--	--	--	--	--	5.97	--	5.87
Conductivity	(µmho/cm)	-	-	-	--	--	--	--	--	--	--	--	--	--	383	--	198

Table 3
Post-Remediation Groundwater Monitoring Data, Loyal 66 Service Station, Loyal, WI
WDNR Project No: 03-10-000388

ABBREVIATIONS, SYMBOLS, & NOTES

PAL: Preventive Action Limit
ES: Enforcement Standard
PQL: Practical Quantitation Limit
GRO: Gasoline Range Organics
DRO: Diesel Range Organics
-: Regulatory limit not established.
--: Not Analyzed N: Not Detected

<"n" denotes not detected where "n" is the detection limit greater than listed under PQL.
V = Full VOC scan performed; no other compounds included in the method were detected.
[1] Listed values are commonly reported minimum PQLs.

Indicates concentration exceeds NR 140 Preventive Action Limit.
Indicates concentration exceeds NR 140 Enforcement Standard.

Well I.D. MW-7

PVC Elevation	1212.65															
Ground Elevation	1213.30	Sample Date			1/5/93	4/12/93	7/20/93	10/6/93	1/6/94	6/8/94	10/5/94	12/30/94	3/31/95	7/12/95	10/16/95	1/16/96
Screen Top Elevation	1208.3	Depth to Water (ft)			5.13	4.21	6.10	4.30	6.63	5.86	6.25	7.46	5.23	7.24	6.85	7.48
Point Elevation	1198.0	Water Elevation (ft)			1207.52	1208.44	1206.55	1208.35	1206.02	1206.79	1206.40	1205.19	1207.42	1205.41	1205.80	1205.17
		Notes:														
ORGANICS		PAL	ES	PQL[1]												
GRO	(µg/L)	-	-	50	1,700	2,490	1,700	1,680	1,290	648	559	503	780	630	430	700
DRO	(µg/L)	-	-	100	--	--	--	--	--	--	--	--	--	--	--	--
Benzene	(µg/L)	0.5	5.0	1	**208**	**283**	**180**	**146**	**139**	**54**	**45**	**39**	**45**	**35**	**31**	**43**
Ethylbenzene	(µg/L)	140	700	1	53	88	68	77	68	19	24	27	32	25	20	34
Toluene	(µg/L)	200	1000	1	26	32	13	8.8	8.7	2.7	2.6	1.6	4.6	3.6	2.4	4.2
o-Xylene/Styrene	(µg/L)	-	-	1	N	38	18	66	7.0	5.4	1.3	2.5	3.7	1.4	1.5	2.6
m- & p- Xylenes	(µg/L)	-	-	1	24	162	96	88	64	34	20	16	26	25	8.6	18
Total Xylenes	(µg/L)	1000	10000	2	24	200	114	154	71	39	22	19	30	26	10	21
Methyl-t-butyl ether	(µg/L)	12	60	3	<10	**17**	<6.0	**46**	N	**16**	**18**	N	N	N	N	N
1,2,4-Trimethylbenzene	(µg/L)	-	-	3	132	129	96	151	75	49	45	27	29	42	15	26
1,3,5-Trimethylbenzene	(µg/L)	-	-	1	30	35	30	33	22	15	11	8.8	10	13	6.5	13
Total Trimethylbenzene	(µg/L)	96	480	4	**162**	**164**	**126**	**184**	**97**	64	55	36	39	55	22	39
FIELD MEASUREMENTS																
Temperature	(°C)	-	-	-	--	--	--	--	--	--	--	--	--	--	--	--
Dissolved Oxygen	(mg/L)	-	-	-	--	--	--	--	--	--	--	--	--	--	--	--
pH	(S.U.)	-	-	-	--	--	--	--	--	--	--	--	--	--	--	--
Conductivity	(µmho/cm)	-	-	-	--	--	--	--	--	--	--	--	--	--	--	--

Table 3
Post-Remediation Groundwater Monitoring Data, Loyal 66 Service Station, Loyal, WI
WDNR Project No: 03-10-000388

ABBREVIATIONS, SYMBOLS, & NOTES

PAL: Preventive Action Limit
ES: Enforcement Standard
PQL: Practical Quantitation Limit
GRO: Gasoline Range Organics
DRO: Diesel Range Organics
-: Regulatory limit not established.
--: Not Analyzed N: Not Detected

<"n" denotes not detected where "n" is the detection limit greater than listed under PQL.
V = Full VOC scan performed; no other compounds included in the method were detected.
[1] Listed values are commonly reported minimum PQLs.

Indicates concentration exceeds NR 140 Preventive Action Limit.
Indicates concentration exceeds NR 140 Enforcement Standard.

Well I.D. MW-7

PVC Elevation	1212.65														
Ground Elevation	1213.30	Sample Date			4/9/96	7/12/96	10/14/96	1/2/97	4/1/97	7/21/97	10/20/97	4/8/98	10/22/98	5/3/99	10/7/99	10/25/00	1/25/01
Screen Top Elevation	1208.3	Depth to Water (ft)			6.50	6.38	6.48	5.64	5.63	6.73	5.60	5.66	6.06	5.70	5.66	5.87	6.09
Point Elevation	1198.0	Water Elevation (ft)			1206.15	1206.27	1206.17	1207.01	1207.02	1205.92	1207.05	1206.99	1206.59	1206.95	1206.99	1206.78	1206.56
		Notes:															
ORGANICS		PAL	ES	PQL[1]													
GRO	(µg/L)	-	-	50	490	570	240	170	260	200	290	280	234	--	169	131	268
DRO	(µg/L)	-	-	100	--	--	--	--	--	--	--	--	--	--	--	--	--
Benzene	(µg/L)	0.5	5.0	1	**24**	**18**	**8.8**	**6.8**	**7.6**	**6.8**	**9.2**	**4.4**	**6.8**	**3.2**	**5.8**	**3.8**	**3.3**
Ethylbenzene	(µg/L)	140	700	1	28	10	4.6	2.0	6.0	3.0	4.5	3.6	2.9	2.2	2.8	1.8	1.4
Toluene	(µg/L)	200	1000	1	3.6	1.7	1.3	0.80	1.1	1.3	2.1	N	N	N	0.73	0.63	0.54
o-Xylene/Styrene	(µg/L)	-	-	1	2.4	1.5	0.60	0.50	0.90	0.60	0.90	N	N	N	0.81	--	--
m- & p- Xylenes	(µg/L)	-	-	1	15	10	2.5	0.40	4.0	2.8	0.60	2.6	N	N	N	--	--
Total Xylenes	(µg/L)	1000	10000	2	17	12	3.1	0.90	4.9	3.4	1.5	2.6	N	N	0.81	<1.7	2.0
Methyl-t-butyl ether	(µg/L)	12	60	3	N	N	N	N	N	N	N	N	N	1.2	N	4.3	<0.091
1,2,4-Trimethylbenzene	(µg/L)	-	-	3	23	30	9.7	5.8	6.8	7.7	10	5.4	7.8	3.6	6.6	2.4	3.3
1,3,5-Trimethylbenzene	(µg/L)	-	-	1	11	10	4.6	1.6	1.8	2.1	4.8	2.0	2.0	N	N	<0.9	0.91
Total Trimethylbenzene	(µg/L)	96	480	4	34	40	14	7.4	8.6	10	15	7.4	10	3.6	6.6	<3.3	4.2
FIELD MEASUREMENTS																	
Temperature	(°C)	-	-	-	--	--	--	--	--	--	--	--	--	--	15.7	15.3	8.2
Dissolved Oxygen	(mg/L)	-	-	-	--	--	--	--	--	--	--	--	--	--	0.1	0.0	0.4
pH	(S.U.)	-	-	-	--	--	--	--	--	--	--	--	--	--	5.35	6.42	5.67
Conductivity	(µmho/cm)	-	-	-	--	--	--	--	--	--	--	--	--	--	510	490	402

Table 3
Post-Remediation Groundwater Monitoring Data, Loyal 66 Service Station, Loyal, WI
WDNR Project No: 03-10-000388

ABBREVIATIONS, SYMBOLS, & NOTES

PAL: Preventive Action Limit
ES: Enforcement Standard
PQL: Practical Quantitation Limit
GRO: Gasoline Range Organics
DRO: Diesel Range Organics
-: Regulatory limit not established.
--: Not Analyzed N: Not Detected

<"n" denotes not detected where "n" is the detection limit greater than listed under PQL.
V = Full VOC scan performed; no other compounds included in the method were detected.
[1] Listed values are commonly reported minimum PQLs.

Indicates concentration exceeds NR 140 Preventive Action Limit.
Indicates concentration exceeds NR 140 Enforcement Standard.

Well I.D. MW-8

PVC Elevation	1213.30															
Ground Elevation	1213.60	Sample Date			1/5/93	4/12/93	7/20/93	10/6/93	1/6/94	6/8/94	10/5/94	12/30/94	3/31/95	7/12/95	10/16/95	1/16/96
Screen Top Elevation	1208.6	Depth to Water (ft)			5.31	4.78	6.40	4.80	7.52	6.58	6.99	8.52	5.68	8.19	7.47	8.20
Point Elevation	1198.6	Water Elevation (ft)			1207.99	1208.52	1206.90	1208.50	1205.78	1206.72	1206.31	1204.78	1207.62	1205.11	1205.83	1205.10
		Notes:														
ORGANICS		PAL	ES	PQL[1]												
GRO	(µg/L)	-	-	50	2,510	5,340	3,200	3,060	2,510	3,340	1,220	1,190	820	2,500	840	1,800
DRO	(µg/L)	-	-	100	--	--	--	--	--	--	--	--	--	--	--	--
Benzene	(µg/L)	0.5	5.0	1	**228**	**461**	**250**	**221**	**130**	**208**	**81**	**69**	**37**	**140**	**40**	**100**
Ethylbenzene	(µg/L)	140	700	1	54	**241**	**163**	134	77	140	41	38	22	N	35	2.7
Toluene	(µg/L)	200	1000	1	89	**246**	116	110	45	73	24	22	6.8	37	12	34
o-Xylene/Styrene	(µg/L)	-	-	1	40	112	69	99	43	82	17	14	6.2	0.90	5.9	15
m- & p- Xylenes	(µg/L)	-	-	1	183	430	281	290	136	224	57	44	25	84	29	40
Total Xylenes	(µg/L)	1000	10000	2	--	542	350	389	179	306	74	58	31	85	35	55
Methyl-t-butyl ether	(µg/L)	12	60	3	<10	**52**	<30	**40**	N	**65**	**20**	N	N	N	N	N
1,2,4-Trimethylbenzene	(µg/L)	-	-	3	77	189	123	181	114	147	49	45	N	38	32	52
1,3,5-Trimethylbenzene	(µg/L)	-	-	1	27	62	39	62	42	53	19	21	12	32	12	26
Total Trimethylbenzene	(µg/L)	96	480	4	**104**	**251**	**162**	**243**	**156**	**200**	68	67	12	70	44	78
FIELD MEASUREMENTS																
Temperature	(°C)	-	-	-	--	--	--	--	--	--	--	--	--	--	--	--
Dissolved Oxygen	(mg/L)	-	-	-	--	--	--	--	--	--	--	--	--	--	--	--
pH	(S.U.)	-	-	-	--	--	--	--	--	--	--	--	--	--	--	--
Conductivity	(µmho/cm)	-	-	-	--	--	--	--	--	--	--	--	--	--	--	--

Table 3
Post-Remediation Groundwater Monitoring Data, Loyal 66 Service Station, Loyal, WI
WDNR Project No: 03-10-000388

ABBREVIATIONS, SYMBOLS, & NOTES

PAL: Preventive Action Limit
ES: Enforcement Standard
PQL: Practical Quantitation Limit
GRO: Gasoline Range Organics
DRO: Diesel Range Organics
-: Regulatory limit not established.
--: Not Analyzed N: Not Detected

<"n" denotes not detected where "n" is the detection limit greater than listed under PQL.
V = Full VOC scan performed; no other compounds included in the method were detected.
[1] Listed values are commonly reported minimum PQLs.

Indicates concentration exceeds NR 140 Preventive Action Limit.
Indicates concentration exceeds NR 140 Enforcement Standard.

Well I.D. MW-8

PVC Elevation	1213.30															
Ground Elevation	1213.60	Sample Date			4/9/96	7/12/96	10/14/96	1/2/97	4/1/97	7/21/97	10/20/97	4/8/98	10/22/98	5/3/99	10/7/99	10/25/00	1/25/01
Screen Top Elevation	1208.6	Depth to Water (ft)			7.35	7.13	7.16	5.97	6.45	7.40	6.89	6.18	6.47	6.11	5.98	6.21	6.47
Point Elevation	1198.6	Water Elevation (ft)			1205.95	1206.17	1206.14	1207.33	1206.85	1205.90	1206.41	1207.12	1206.83	1207.19	1207.32	1207.05	1206.83
		Notes:															
ORGANICS		PAL	ES	PQL[1]													
GRO	(µg/L)	-	-	50	1,500	3,500	1,700	1,200	2,200	2,000	1,700	1,800	2,380	--	1,140	1,440	4,900
DRO	(µg/L)	-	-	100	--	--	--	--	--	--	--	--	--	--	--	--	--
Benzene	(µg/L)	0.5	5.0	1	**84**	**190**	**96**	**91**	**120**	**110**	**130**	**110**	**127**	**150**	**79**	**73**	**115**
Ethylbenzene	(µg/L)	140	700	1	68	**180**	63	58	66	110	94	100	111	**158**	78	89	**183**
Toluene	(µg/L)	200	1000	1	30	65	29	23	36	33	32	34	35	54	19	18	47
o-Xylene/Styrene	(µg/L)	-	-	1	12	37	18	43	20	20	19	17	14	24	7.0	--	--
m- & p- Xylenes	(µg/L)	-	-	1	57	120	55	11	72	68	50	74	55	105	37	--	--
Total Xylenes	(µg/L)	1000	10000	2	69	157	73	54	92	88	69	91	68	129	44	57	275
Methyl-t-butyl ether	(µg/L)	12	60	3	N	N	N	N	N	N	N	N	N	N	N	11	<1.8
1,2,4-Trimethylbenzene	(µg/L)	-	-	3	47	96	43	29	48	52	42	45	44	77	32	42	178
1,3,5-Trimethylbenzene	(µg/L)	-	-	1	23	47	23	12	24	25	20	22	24	37	11	12	68
Total Trimethylbenzene	(µg/L)	96	480	4	70	**143**	66	41	72	77	62	67	67	**114**	43	54	**246**
FIELD MEASUREMENTS																	
Temperature	(°C)	-	-	-	--	--	--	--	--	--	--	--	--	--	16.0	15.5	8.3
Dissolved Oxygen	(mg/L)	-	-	-	--	--	--	--	--	--	--	--	--	--	0.2	0.0	0.0
pH	(S.U.)	-	-	-	--	--	--	--	--	--	--	--	--	--	6.47	6.58	5.51
Conductivity	(µmho/cm)	-	-	-	--	--	--	--	--	--	--	--	--	--	550	660	550

Table 3
Post-Remediation Groundwater Monitoring Data, Loyal 66 Service Station, Loyal, WI
WDNR Project No: 03-10-000388

ABBREVIATIONS, SYMBOLS, & NOTES

PAL: Preventive Action Limit
ES: Enforcement Standard
PQL: Practical Quantitation Limit
GRO: Gasoline Range Organics
DRO: Diesel Range Organics
-: Regulatory limit not established.
--: Not Analyzed N: Not Detected

<"n" denotes not detected where "n" is the detection limit greater than listed under PQL.
V = Full VOC scan performed; no other compounds included in the method were detected.
[1] Listed values are commonly reported minimum PQLs.

Indicates concentration exceeds NR 140 Preventive Action Limit.
Indicates concentration exceeds NR 140 Enforcement Standard.

Well I.D. MW-9

PVC Elevation	1211.48															
Ground Elevation	1211.90	Sample Date			1/5/93	4/12/93	7/20/93	10/6/93	1/6/94	6/8/94	10/5/94	12/30/94	3/31/95	7/12/95	10/16/95	1/16/96
Screen Top Elevation	1206.4	Depth to Water (ft)			5.22	4.49	5.37	4.42	--	6.53	5.61	6.20	4.87	6.01	5.78	6.14
Point Elevation	1196.4	Water Elevation (ft)			1206.26	1206.99	1206.11	1207.06		1204.95	1205.87	1205.28	1206.61	1205.47	1205.70	1205.34
		Notes:														
ORGANICS		PAL	ES	PQL[1]												
GRO	(µg/L)	-	-	50	<10	<50	<50	<50	--	<50	--	<50	--	N	N	N
DRO	(µg/L)	-	-	100	--	--	--	--	--	--	--	--	--	--	--	--
Benzene	(µg/L)	0.5	5.0	1	N	N	N	N	--	N	--	N	--	N	N	N
Ethylbenzene	(µg/L)	140	700	1	N	N	N	N	--	N	--	N	--	N	N	N
Toluene	(µg/L)	200	1000	1	N	N	N	N	--	N	--	N	--	0.60	0.80	N
o-Xylene/Styrene	(µg/L)	-	-	1	N	N	N	N	--	N	--	N	--	N	N	N
m- & p- Xylenes	(µg/L)	-	-	1	N	N	N	N	--	N	--	N	--	N	N	N
Total Xylenes	(µg/L)	1000	10000	2	N	N	N	N	--	N	--	N	--	N	N	N
Methyl-t-butyl ether	(µg/L)	12	60	3	<10	N	N	N	--	N	--	N	--	N	N	N
1,2,4-Trimethylbenzene	(µg/L)	-	-	3	N	N	N	N	--	N	--	N	--	N	N	N
1,3,5-Trimethylbenzene	(µg/L)	-	-	1	N	N	N	N	--	N	--	N	--	N	N	N
Total Trimethylbenzene	(µg/L)	96	480	4	N	N	N	N	--	N	--	N	--	N	N	N
FIELD MEASUREMENTS																
Temperature	(°C)	-	-	-	--	--	--	--	--	--	--	--	--	--	--	--
Dissolved Oxygen	(mg/L)	-	-	-	--	--	--	--	--	--	--	--	--	--	--	--
pH	(S.U.)	-	-	-	--	--	--	--	--	--	--	--	--	--	--	--
Conductivity	(µmho/cm)	-	-	-	--	--	--	--	--	--	--	--	--	--	--	--

Table 3
Post-Remediation Groundwater Monitoring Data, Loyal 66 Service Station, Loyal, WI
WDNR Project No: 03-10-000388

ABBREVIATIONS, SYMBOLS, & NOTES

PAL: Preventive Action Limit
ES: Enforcement Standard
PQL: Practical Quantitation Limit
GRO: Gasoline Range Organics
DRO: Diesel Range Organics
-: Regulatory limit not established.
--: Not Analyzed N: Not Detected

<"n" denotes not detected where "n" is the detection limit greater than listed under PQL.
V = Full VOC scan performed; no other compounds included in the method were detected.
[1] Listed values are commonly reported minimum PQLs.

Indicates concentration exceeds NR 140 Preventive Action Limit.
Indicates concentration exceeds NR 140 Enforcement Standard.

Well I.D. MW-9

PVC Elevation	1211.48																
Ground Elevation	1211.90	Sample Date			4/9/96	7/12/96	10/14/96	1/2/97	4/1/97	7/21/97	10/20/97	4/8/98	10/22/98	5/3/99	10/7/99	10/25/00	1/25/01
Screen Top Elevation	1206.4	Depth to Water (ft)			5.32	5.67	5.84	5.28	4.64	5.75	5.25	5.17	5.60	5.46	5.39	5.51	5.57
Point Elevation	1196.4	Water Elevation (ft)			1206.16	1205.81	1205.64	1206.20	1206.84	1205.73	1206.23	1206.31	1205.88	1206.02	1206.09	1205.97	1205.91
		Notes:															
ORGANICS		PAL	ES	PQL[1]													
GRO	(µg/L)	-	-	50	N	--	27	--	N	N	N	--	N	--	N	<17	<5.9
DRO	(µg/L)	-	-	100	--	--	--	--	--	--	--	--	--	--	--	--	--
Benzene	(µg/L)	0.5	5.0	1	N	--	N	--	N	N	N	--	N	N	N	<0.5	<.21
Ethylbenzene	(µg/L)	140	700	1	N	--	N	--	N	N	N	--	N	N	N	<0.6	<0.23
Toluene	(µg/L)	200	1000	1	N	--	N	--	N	N	N	--	N	N	N	<0.6	<0.22
o-Xylene/Styrene	(µg/L)	-	-	1	N	--	N	--	N	N	N	--	N	N	N	--	--
m- & p- Xylenes	(µg/L)	-	-	1	N	--	N	--	N	N	N	--	N	N	N	--	--
Total Xylenes	(µg/L)	1000	10000	2	N	--	N	--	N	N	N	--	N	N	N	<1.7	<0.44
Methyl-t-butyl ether	(µg/L)	12	60	3	N	--	N	--	N	N	N	--	N	N	N	<0.92	<0.091
1,2,4-Trimethylbenzene	(µg/L)	-	-	3	N	--	N	--	N	N	N	--	N	N	N	<1.7	<.23
1,3,5-Trimethylbenzene	(µg/L)	-	-	1	N	--	N	--	N	N	N	--	N	N	N	<0.9	<0.21
Total Trimethylbenzene	(µg/L)	96	480	4	N	--	N	--	N	N	N	--	N	N	N	<2.6	<0.44
FIELD MEASUREMENTS																	
Temperature	(°C)	-	-	-	--	--	--	--	--	--	--	--	--	--	13.6	13.5	9.6
Dissolved Oxygen	(mg/L)	-	-	-	--	--	--	--	--	--	--	--	--	--	3.1	3.3	4.4
pH	(S.U.)	-	-	-	--	--	--	--	--	--	--	--	--	--	6.60	6.68	6.45
Conductivity	(µmho/cm)	-	-	-	--	--	--	--	--	--	--	--	--	--	540	500	469

Table 3
Post-Remediation Groundwater Monitoring Data, Loyal 66 Service Station, Loyal, WI
WDNR Project No: 03-10-000388

ABBREVIATIONS, SYMBOLS, & NOTES

PAL: Preventive Action Limit
ES: Enforcement Standard
PQL: Practical Quantitation Limit
GRO: Gasoline Range Organics
DRO: Diesel Range Organics
-: Regulatory limit not established.
--: Not Analyzed N: Not Detected

<"n" denotes not detected where "n" is the detection limit greater than listed under PQL.
V = Full VOC scan performed; no other compounds included in the method were detected.
[1] Listed values are commonly reported minimum PQLs.

Indicates concentration exceeds NR 140 Preventive Action Limit.
Indicates concentration exceeds NR 140 Enforcement Standard.

Well I.D. PW-2

PVC Elevation	1212.98															
Ground Elevation	1213.65	Sample Date			1/5/93	4/12/93	7/20/93	10/6/93	1/6/94	6/8/94	10/5/94	12/30/94	3/31/95	7/12/95	10/16/95	1/16/96
Screen Top Elevation		Depth to Water (ft)			--	--	--	--	--	--	--	5.44	--	--	--	--
Point Elevation		Water Elevation (ft)										1207.54				
		Notes:														
ORGANICS		PAL	ES	PQL[1]												
GRO	(µg/L)	-	-	50	--	--	--	--	--	54	N	<50	--	62	--	22
DRO	(µg/L)	-	-	100	--	--	--	--	--	--	--	--	--	--	--	--
Benzene	(µg/L)	0.5	5.0	1	--	--	--	--	--	**5.1**	**1.2**	**1.2**	--	**9.1**	--	**2.4**
Ethylbenzene	(µg/L)	140	700	1	--	--	--	--	--	N	N	N	--	1.4	--	N
Toluene	(µg/L)	200	1000	1	--	--	--	--	--	2.2	N	N	--	3.3	--	0.50
o-Xylene/Styrene	(µg/L)	-	-	1	--	--	--	--	--	N	N	N	--	1.1	--	N
m- & p- Xylenes	(µg/L)	-	-	1	--	--	--	--	--	1.1	N	N	--	3.6	--	0.80
Total Xylenes	(µg/L)	1000	10000	2	--	--	--	--	--	1.1	N	N	--	4.7	--	0.80
Methyl-t-butyl ether	(µg/L)	12	60	3	--	--	--	--	--	3.2	N	N	--	N	--	N
1,2,4-Trimethylbenzene	(µg/L)	-	-	3	--	--	--	--	--	N	N	N	--	1.4	--	N
1,3,5-Trimethylbenzene	(µg/L)	-	-	1	--	--	--	--	--	N	N	N	--	N	--	N
Total Trimethylbenzene	(µg/L)	96	480	4	--	--	--	--	--	N	N	N	--	1.4	--	N
FIELD MEASUREMENTS																
Temperature	(°C)	-	-	-	--	--	--	--	--	--	--	--	--	--	--	--
Dissolved Oxygen	(mg/L)	-	-	-	--	--	--	--	--	--	--	--	--	--	--	--
pH	(S.U.)	-	-	-	--	--	--	--	--	--	--	--	--	--	--	--
Conductivity	(µmho/cm)	-	-	-	--	--	--	--	--	--	--	--	--	--	--	--

Table 3
Post-Remediation Groundwater Monitoring Data, Loyal 66 Service Station, Loyal, WI
WDNR Project No: 03-10-000388

ABBREVIATIONS, SYMBOLS, & NOTES

PAL: Preventive Action Limit
ES: Enforcement Standard
PQL: Practical Quantitation Limit
GRO: Gasoline Range Organics
DRO: Diesel Range Organics
-: Regulatory limit not established.
--: Not Analyzed N: Not Detected

<"n" denotes not detected where "n" is the detection limit greater than listed under PQL.
V = Full VOC scan performed; no other compounds included in the method were detected.
[1] Listed values are commonly reported minimum PQLs.

Indicates concentration exceeds NR 140 Preventive Action Limit.
Indicates concentration exceeds NR 140 Enforcement Standard.

Well I.D. PW-2

PVC Elevation	1212.98																
Ground Elevation	1213.65	Sample Date			4/9/96	7/12/96	10/14/96	1/2/97	4/1/97	7/21/97	10/20/97	4/8/98	10/22/98	5/3/99	10/7/99	10/25/00	1/25/01
Screen Top Elevation		Depth to Water (ft)			--	--	--	--	--	--	--	--	--	--	--	--	--
Point Elevation		Water Elevation (ft)															
		Notes:															
ORGANICS		PAL	ES	PQL[1]													
GRO	(µg/L)	-	-	50	52	--	65	--	64	--	43	27	--	--	--	--	--
DRO	(µg/L)	-	-	100	--	--	--	--	--	--	--	--	--	--	--	--	--
Benzene	(µg/L)	0.5	5.0	1	**1.2**	--	**5.1**	--	**2.4**	--	**5.9**	**0.90**	--	--	--	--	--
Ethylbenzene	(µg/L)	140	700	1	N	--	1.1	--	0.60	--	0.80	0.20	--	--	--	--	--
Toluene	(µg/L)	200	1000	1	0.80	--	1.6	--	1.3	--	0.80	0.50	--	--	--	--	--
o-Xylene/Styrene	(µg/L)	-	-	1	1.5	--	0.60	--	0.90	--	0.50	N	--	--	--	--	--
m- & p- Xylenes	(µg/L)	-	-	1	2.7	--	2.2	--	1.8	--	1.2	0.50	--	--	--	--	--
Total Xylenes	(µg/L)	1000	10000	2	4.2	--	2.8	--	2.7	--	1.7	0.50	--	--	--	--	--
Methyl-t-butyl ether	(µg/L)	12	60	3	N	--	N	--	N	--	N	N	--	--	--	--	--
1,2,4-Trimethylbenzene	(µg/L)	-	-	3	1.2	--	1.1	--	0.90	--	0.80	N	--	--	--	--	--
1,3,5-Trimethylbenzene	(µg/L)	-	-	1	1.3	--	0.40	--	0.60	--	N	N	--	--	--	--	--
Total Trimethylbenzene	(µg/L)	96	480	4	1.5	--	1.5	--	1.5	--	0.80	N	--	--	--	--	--
FIELD MEASUREMENTS																	
Temperature	(°C)	-	-	-	--	--	--	--	--	--	--	--	--	--	--	--	--
Dissolved Oxygen	(mg/L)	-	-	-	--	--	--	--	--	--	--	--	--	--	--	--	--
pH	(S.U.)	-	-	-	--	--	--	--	--	--	--	--	--	--	--	--	--
Conductivity	(µmho/cm)	-	-	-	--	--	--	--	--	--	--	--	--	--	--	--	--

Table 3
Post-Remediation Groundwater Monitoring Data, Loyal 66 Service Station, Loyal, WI
WDNR Project No: 03-10-000388

ABBREVIATIONS, SYMBOLS, & NOTES

PAL: Preventive Action Limit
ES: Enforcement Standard
PQL: Practical Quantitation Limit
GRO: Gasoline Range Organics
DRO: Diesel Range Organics
-: Regulatory limit not established.
--: Not Analyzed N: Not Detected

<"n" denotes not detected where "n" is the detection limit greater than listed under PQL.
V = Full VOC scan performed; no other compounds included in the method were detected.
[1] Listed values are commonly reported minimum PQLs.

Indicates concentration exceeds NR 140 Preventive Action Limit.
Indicates concentration exceeds NR 140 Enforcement Standard.

Well I.D. Field Blank

		Sample Date			1/5/93	4/12/93	7/20/93	10/6/93	1/6/94	6/8/94	10/5/94	12/30/94	3/31/95	7/12/95	10/16/95	1/16/96
		Sample I.D.			MW-30	MW-30	MW-30	MW-30	MW-30	MW-30	MW-30	MW-30	MW-30	MW-30	MW-30	MW-30
		Notes:														
ORGANICS		PAL	ES	PQL[1]												
GRO	(µg/L)	-	-	50	<10	<50	<50	<50	<50	<50	N	<50	<45	N	N	N
DRO	(µg/L)	-	-	100	--	--	--		--	--	--	--	--	--	--	--
Benzene	(µg/L)	0.5	5.0	1	N	N	N	N	N	N	N	N	N	N	N	N
Ethylbenzene	(µg/L)	140	700	1	N	N	N	N	N	N	N	N	N	N	N	N
Toluene	(µg/L)	200	1000	1	N	N	N	N	N	N	N	N	N	N	N	N
o-Xylene/Styrene	(µg/L)	-	-	1	N	N	N	N	N	N	N	N	N	N	N	N
m- & p- Xylenes	(µg/L)	-	-	1	N	N	N	N	N	N	N	N	N	N	N	N
Total Xylenes	(µg/L)	1000	10000	2	--	N	N	N	N	N	N	N	N	N	N	N
Methyl-t-butyl ether	(µg/L)	12	60	3	<10	N	N	N	N	N	N	N	N	N	N	N
1,2,4-Trimethylbenzene	(µg/L)	-	-	3	N	N	N	N	N	N	N	N	N	N	N	N
1,3,5-Trimethylbenzene	(µg/L)	-	-	1	N	N	N	N	N	N	N	N	N	N	N	N
Total Trimethylbenzene	(µg/L)	96	480	4	N	N	N	N	N	N	N	N	N	N	N	N
FIELD MEASUREMENTS																
Temperature	(°C)	-	-	-	--	--	--	--	--	--	--	--	--	--	--	--
Dissolved Oxygen	(mg/L)	-	-	-	--	--	--	--	--	--	--	--	--	--	--	--
pH	(S.U.)	-	-	-	--	--	--	--	--	--	--	--	--	--	--	--
Conductivity	(µmho/cm)	-	-	-	--	--	--	--	--	--	--	--	--	--	--	--

Table 3
Post-Remediation Groundwater Monitoring Data, Loyal 66 Service Station, Loyal, WI
WDNR Project No: 03-10-000388

ABBREVIATIONS, SYMBOLS, & NOTES

PAL: Preventive Action Limit
ES: Enforcement Standard
PQL: Practical Quantitation Limit
GRO: Gasoline Range Organics
DRO: Diesel Range Organics
-: Regulatory limit not established.
--: Not Analyzed N: Not Detected

<"n" denotes not detected where "n" is the detection limit greater than listed under PQL.
V = Full VOC scan performed; no other compounds included in the method were detected.
[1] Listed values are commonly reported minimum PQLs.

Indicates concentration exceeds NR 140 Preventive Action Limit.
Indicates concentration exceeds NR 140 Enforcement Standard.

Well I.D. Field Blank

		Sample Date			4/9/96	7/12/96	10/14/96	1/2/97	4/1/97	7/21/97	10/20/97	4/8/98	10/22/98	5/3/99	10/7/99	10/25/00	1/25/01
		Sample I.D.			MW-30	MW-30	MW-30	MW-30	MW-30	MW-30	MW-30	MW-30	MW-30	MW-30	MW-30	MW-30	MW-30
		Notes:															
ORGANICS		PAL	ES	PQL[1]													
GRO	(µg/L)	-	-	50	N	N	N	N	N	N	N	N	N	--	N	<17	<5.9
DRO	(µg/L)	-	-	100	--	--	--	--	--	--	--	--	--	--	--	--	--
Benzene	(µg/L)	0.5	5.0	1	N	N	N	N	N	N	N	N	N	N	N	<0.5	<.21
Ethylbenzene	(µg/L)	140	700	1	N	N	N	N	N	N	N	N	N	N	N	<0.6	<0.23
Toluene	(µg/L)	200	1000	1	N	N	N	N	N	N	N	N	N	N	N	<0.6	<0.22
o-Xylene/Styrene	(µg/L)	-	-	1	N	N	N	N	N	N	N	N	N	N	N	--	--
m- & p- Xylenes	(µg/L)	-	-	1	N	N	N	N	N	N	N	N	N	N	N	--	--
Total Xylenes	(µg/L)	1000	10000	2	N	N	N	N	N	N	N	N	N	N	N	<1.7	<0.44
Methyl-t-butyl ether	(µg/L)	12	60	3	N	N	N	N	N	N	N	N	N	N	N	<0.92	<0.091
1,2,4-Trimethylbenzene	(µg/L)	-	-	3	N	N	N	N	N	N	N	N	N	N	N	<1.7	<.23
1,3,5-Trimethylbenzene	(µg/L)	-	-	1	N	N	N	N	N	N	N	N	N	N	N	<0.9	<0.21
Total Trimethylbenzene	(µg/L)	96	480	4	N	N	N	N	N	N	N	N	N	N	N	<2.6	<0.44
FIELD MEASUREMENTS																	
Temperature	(°C)	-	-	-	--	--	--	--	--	--	--	--	--	--	12.7	--	--
Dissolved Oxygen	(mg/L)	-	-	-	--	--	--	--	--	--	--	--	--	--	--	--	--
pH	(S.U.)	-	-	-	--	--	--	--	--	--	--	--	--	--	6.49	--	--
Conductivity	(µmho/cm)	-	-	-	--	--	--	--	--	--	--	--	--	--	0	--	--

Table 3
Post-Remediation Groundwater Monitoring Data, Loyal 66 Service Station, Loyal, WI
WDNR Project No: 03-10-000388

ABBREVIATIONS, SYMBOLS, & NOTES

PAL: Preventive Action Limit
ES: Enforcement Standard
PQL: Practical Quantitation Limit
GRO: Gasoline Range Organics
DRO: Diesel Range Organics
-: Regulatory limit not established.
--: Not Analyzed N: Not Detected

<"n" denotes not detected where "n" is the detection limit greater than listed under PQL.
V = Full VOC scan performed; no other compounds included in the method were detected.
[1] Listed values are commonly reported minimum PQLs.

Indicates concentration exceeds NR 140 Preventive Action Limit.
Indicates concentration exceeds NR 140 Enforcement Standard.

Well I.D. Duplicate Sample

	Sample Date				1/5/93	4/12/93	7/20/93	10/6/93	1/6/94	6/8/94	10/5/94	12/30/94	3/31/95	7/12/95	10/16/95	1/16/96
	Sample I.D.				MW-5	MW-2	MW-2	MW-2	MW-2	MW-8	MW-7	MW-9	MW-6	MW-9	MW-7	MW-6
	Notes:															
ORGANICS		PAL	ES	PQL[1]												
GRO	(µg/L)	-	-	50	<10	9,390	21,000	33,000	17,900	3,940	556	<50	N	N	470	N
DRO	(µg/L)	-	-	100	--	--	--	--	--	--	--	--	--	--	--	--
Benzene	(µg/L)	0.5	5.0	1	N	**121**	**652**	**96**	**920**	**172**	**46**	N	N	N	**34**	N
Ethylbenzene	(µg/L)	140	700	1	N	**217**	**822**	**598**	**650**	114	24	N	N	N	22	N
Toluene	(µg/L)	200	1000	1	N	**360**	**1,370**	**505**	**1,170**	61	2.8	N	N	0.80	3.0	N
o-Xylene/Styrene	(µg/L)	-	-	1	N	245	762	868	584	83	1.1	N	N	N	1.8	N
m- & p- Xylenes	(µg/L)	-	-	1	N	780	2,070	2,880	2,030	220	21	N	N	N	10	N
Total Xylenes	(µg/L)	1000	10000	2	--	**1,025**	**2,832**	**3,748**	**2,614**	303	21	N	N	N	12	N
Methyl-t-butyl ether	(µg/L)	12	60	3	<10	**150**	**505**	<30	<30	**58**	**18**	N	N	N	N	N
1,2,4-Trimethylbenzene	(µg/L)	-	-	3	N	370	841	1,540	970	144	46	N	N	N	19	N
1,3,5-Trimethylbenzene	(µg/L)	-	-	1	N	132	253	598	294	54	11	N	N	N	8.9	N
Total Trimethylbenzene	(µg/L)	96	480	4	N	**502**	**1,094**	**2,138**	**1,264**	**198**	57	N	N	N	28	N
FIELD MEASUREMENTS																
Temperature	(°C)	-	-	-	--	--	--	--	--	--	--	--	--	--	--	--
Dissolved Oxygen	(mg/L)	-	-	-	--	--	--	--	--	--	--	--	--	--	--	--
pH	(S.U.)	-	-	-	--	--	--	--	--	--	--	--	--	--	--	--
Conductivity	(µmho/cm)	-	-	-	--	--	--	--	--	--	--	--	--	--	--	--

Table 3
Post-Remediation Groundwater Monitoring Data, Loyal 66 Service Station, Loyal, WI
WDNR Project No: 03-10-000388

ABBREVIATIONS, SYMBOLS, & NOTES

PAL: Preventive Action Limit
ES: Enforcement Standard
PQL: Practical Quantitation Limit
GRO: Gasoline Range Organics
DRO: Diesel Range Organics
-: Regulatory limit not established.
--: Not Analyzed N: Not Detected

<"n" denotes not detected where "n" is the detection limit greater than listed under PQL.
V = Full VOC scan performed; no other compounds included in the method were detected.
[1] Listed values are commonly reported minimum PQLs.

Indicates concentration exceeds NR 140 Preventive Action Limit.
Indicates concentration exceeds NR 140 Enforcement Standard.

Well I.D. Duplicate Sample

		Sample Date			4/9/96	7/12/96	10/14/96	1/2/97	4/1/97	7/21/97	10/20/97	4/8/98	10/22/98	5/3/99	10/7/99		
		Sample I.D.			MW-7	MW-6	MW-8	MW-8	MW-2	MW-40	MW-40	MW-40	MW-40	MW-40	MW-40		
		Notes:															
ORGANICS		PAL	ES	PQL[1]													
GRO	(µg/L)	-	-	50	490	N	1,700	1,100	5,200	180	360	250	2,210	--	238		
DRO	(µg/L)	-	-	100	--	--	--	--	--	--	--	--	--	--	--		
Benzene	(µg/L)	0.5	5.0	1	**24**	N	**100**	**88**	**22**	**6.4**	**9.0**	**4.4**	**85**	**143**	**6.8**		
Ethylbenzene	(µg/L)	140	700	1	28	N	66	57	40	1.2	2.2	3.4	86	**152**	3.3		
Toluene	(µg/L)	200	1000	1	3.6	N	31	20	25	2.9	4.6	N	26	54	0.85		
o-Xylene/Styrene	(µg/L)	-	-	1	2.4	N	19	41	69	2.4	0.90	N	10	25	0.94		
m- & p- Xylenes	(µg/L)	-	-	1	15	N	54	11	150	0.40	0.60	2.4	40	106	N		
Total Xylenes	(µg/L)	1000	10000	2	17	N	73	52	219	2.8	1.5	2.4	50	131	0.94		
Methyl-t-butyl ether	(µg/L)	12	60	3	N	N	N	N	N	N	N	N	N	N	N		
1,2,4-Trimethylbenzene	(µg/L)	-	-	3	23	N	43	29	170	6.5	11	4.6	32	77	8.8		
1,3,5-Trimethylbenzene	(µg/L)	-	-	1	11	N	24	13	86	1.7	5.2	1.7	20	37	N		
Total Trimethylbenzene	(µg/L)	96	480	4	34	N	67	42	**256**	8.2	16	6.3	52	**114**	8.8		
FIELD MEASUREMENTS																	
Temperature	(°C)	-	-	-	--	--	--	--	--	--	--	--	--	--	15.3		
Dissolved Oxygen	(mg/L)	-	-	-	--	--	--	--	--	--	--	--	--	--	--		
pH	(S.U.)	-	-	-	--	--	--	--	--	--	--	--	--	--	6.36		
Conductivity	(µmho/cm)	-	-	-	--	--	--	--	--	--	--	--	--	--	505		

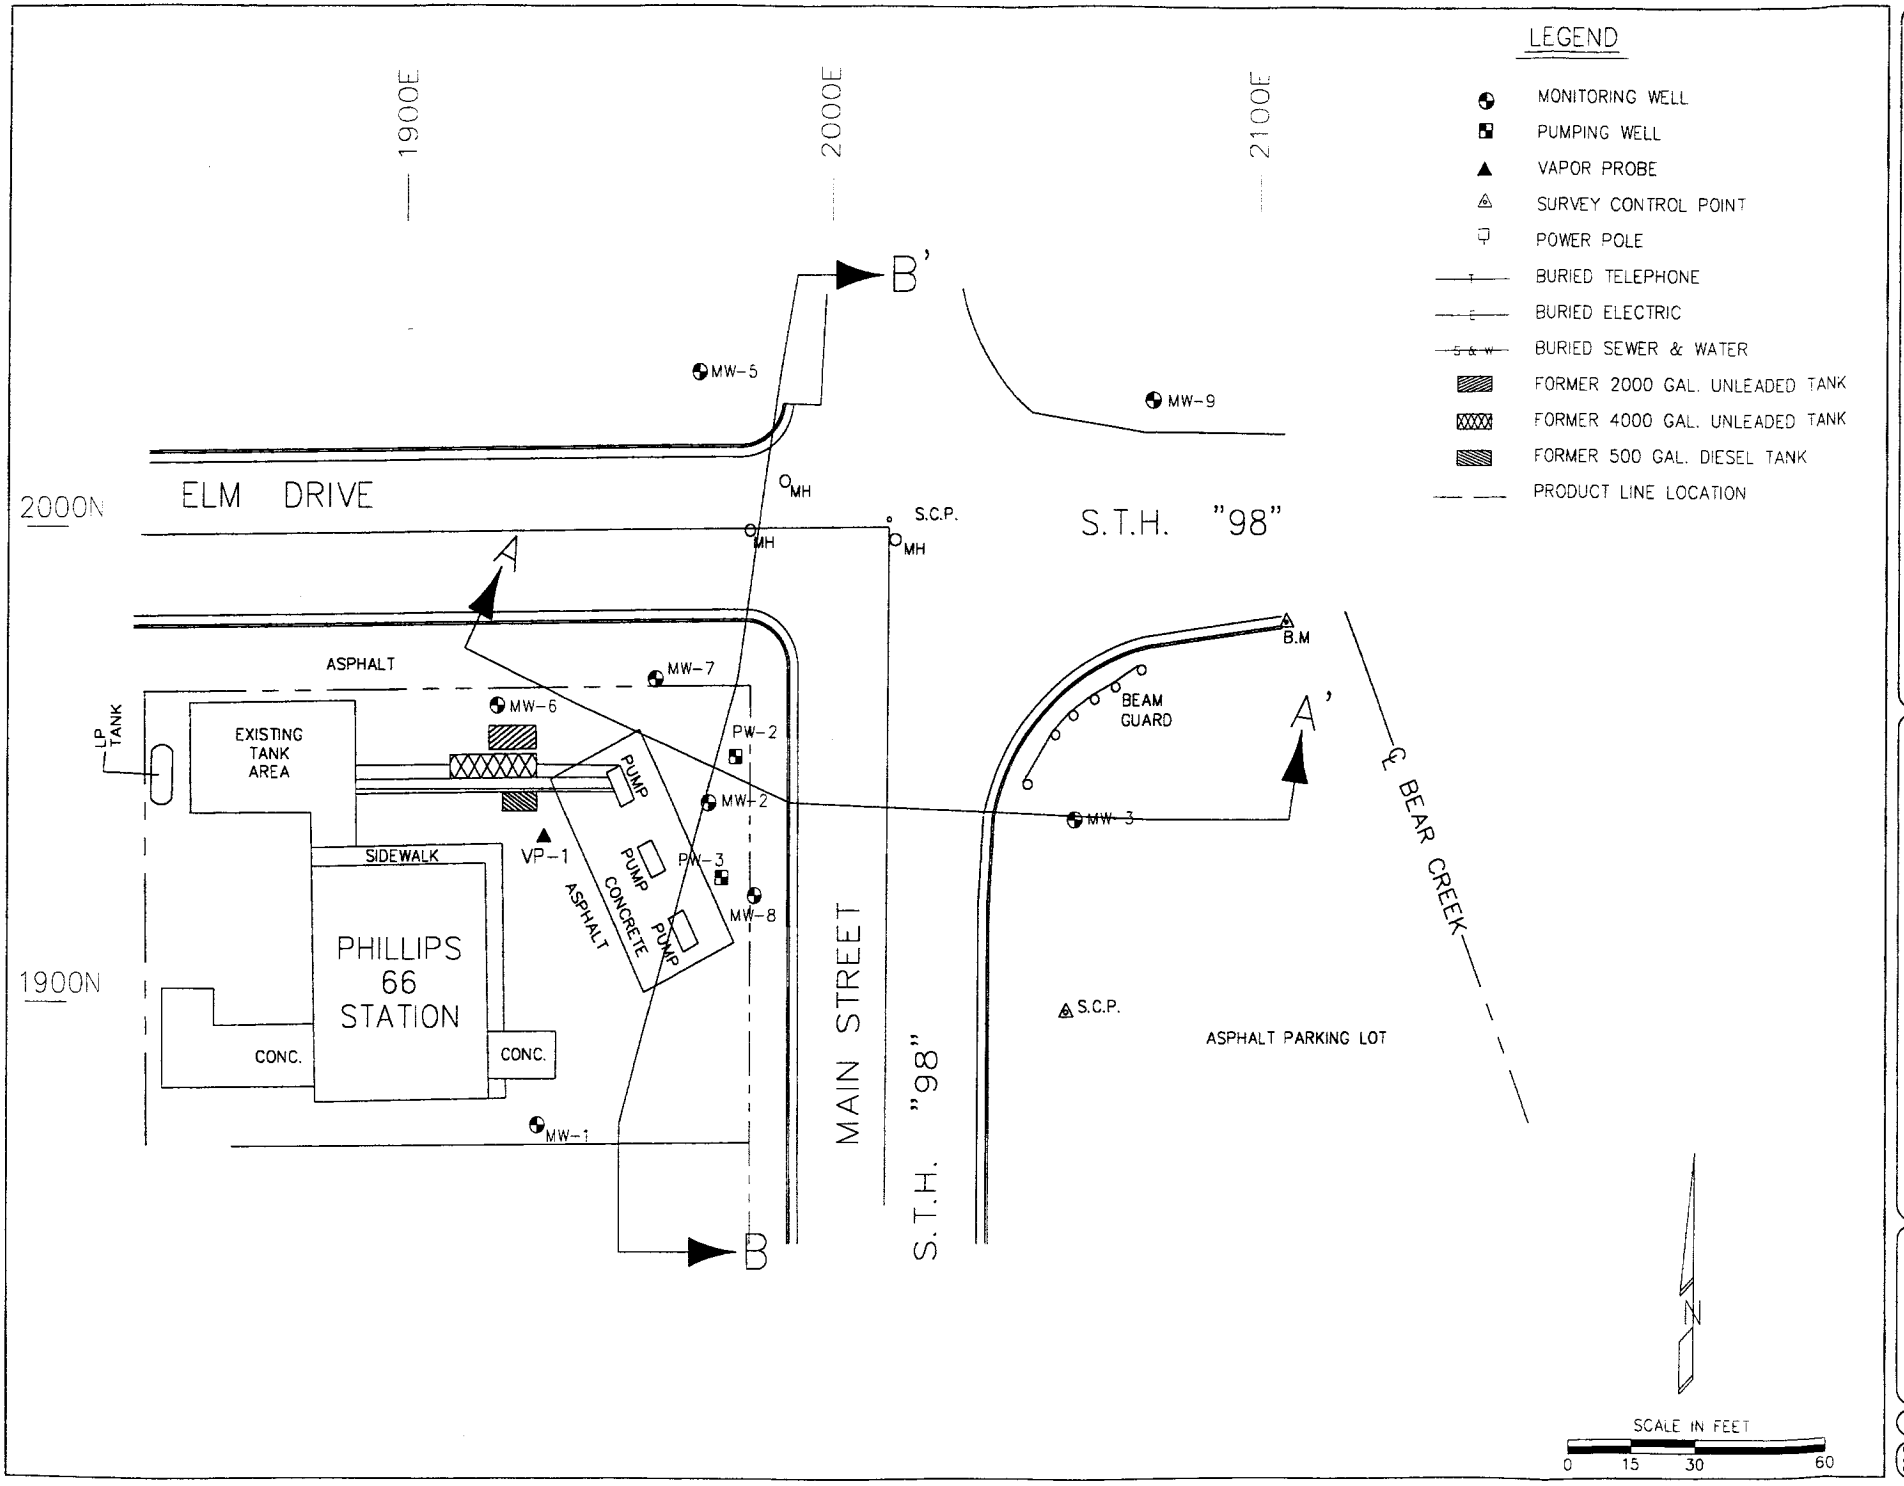

CENTRAL WISCONSIN ENGINEERS AND ARCHITECTS, INC.
5707 SCHOFIELD AVENUE WESTON, WISCONSIN 54476
PHONE: (715) 359-9400 FAX: (715) 355-4199

PROJECT:

CROSS SECTION
LOCATION MAP
LOYAL 66 SERVICE STATION
LOYAL, WISCONSIN

DRAWN BY: H.S.
CHECKED BY: P.S.
APPROVED BY:
DATE: 05/00
PROJECT NO: 13090070
DNR NO: 03-10-000388

FIGURE:

CAD FILE:

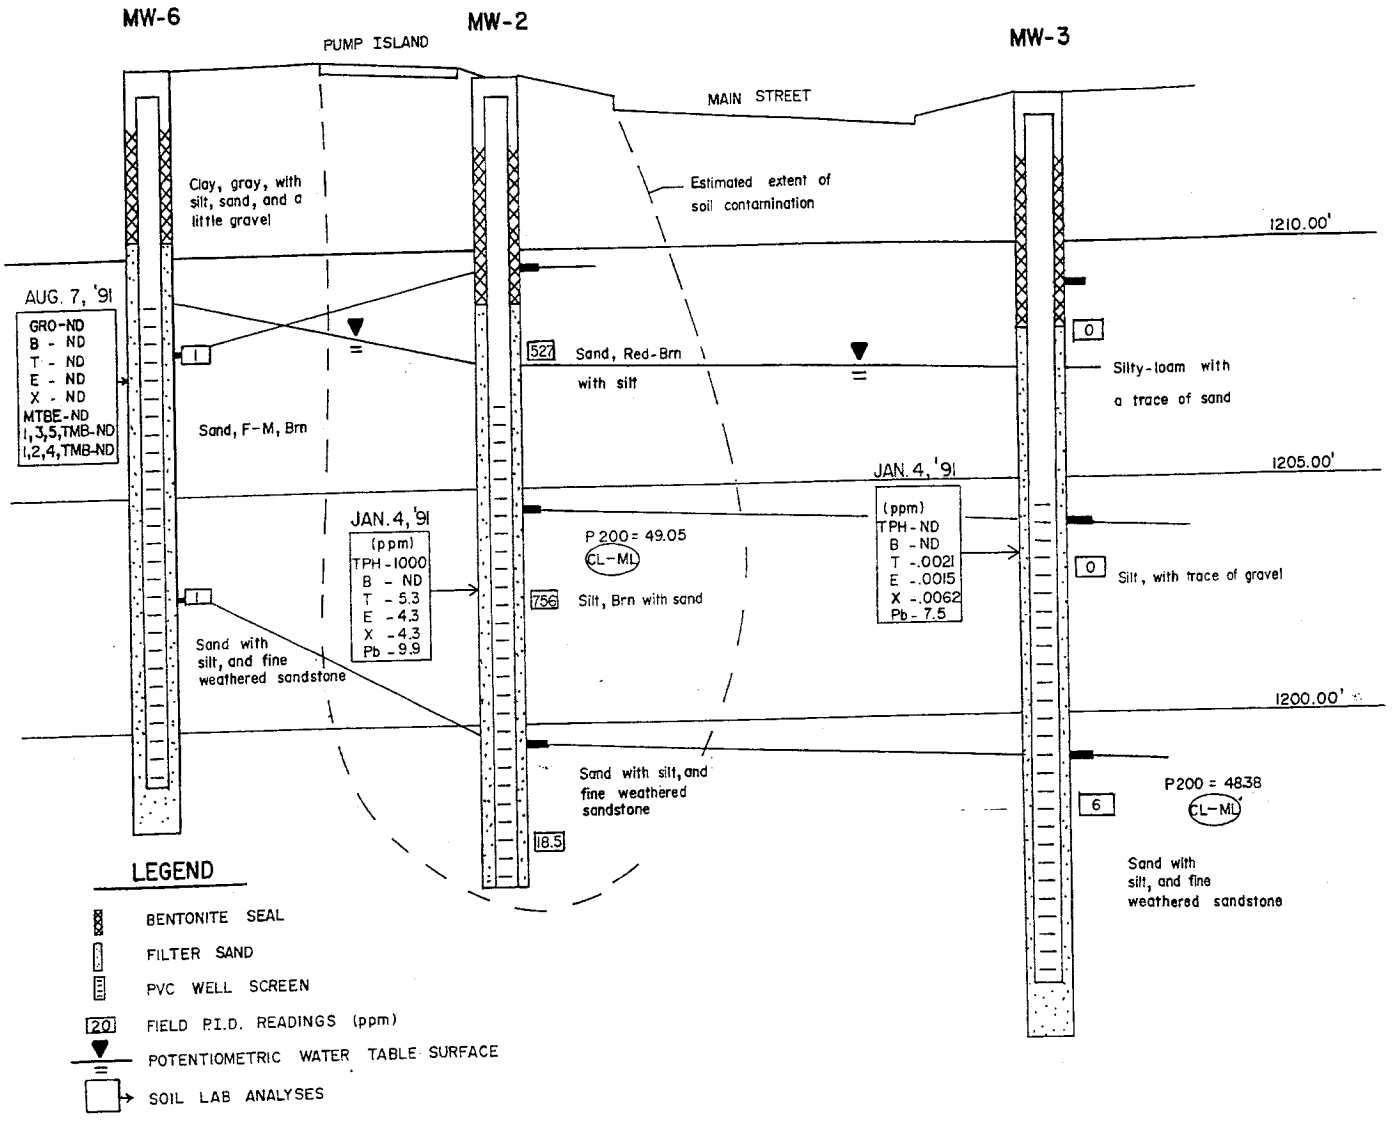

CENTRAL WISCONSIN ENGINEERS AND ARCHITECTS, INC.
5707 SCHOFIELD AVENUE WESTON, WISCONSIN 54476
PHONE: (715) 359-9400 FAX: (715) 355-4199

PROJECT:

CROSS SECTION A-A'
LOYAL 66 SERVICE STATION
LOYAL, WISCONSIN

DRAWN BY: H.S.
CHECKED BY:
APPROVED BY:
DATE: CWE 05/0
PROJECT NO: 13090070
DNR NO: 03-10-000366

FIGURE:

CAD FILE:

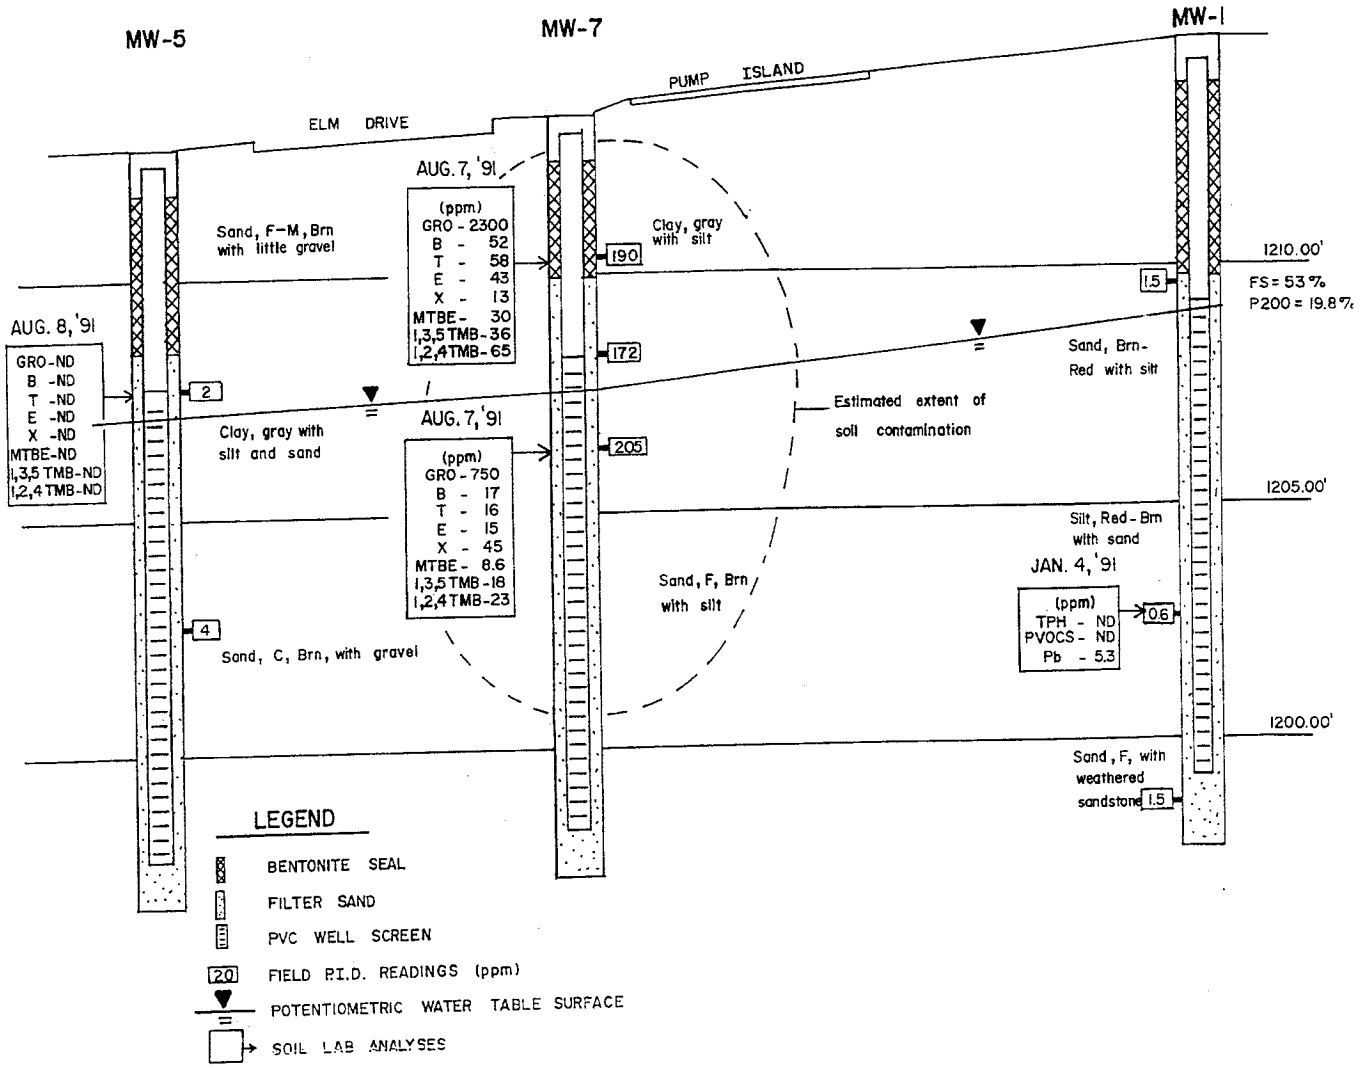

CENTRAL WISCONSIN ENGINEERS AND ARCHITECTS, INC.

CROSS SECTION B-B'
LOYAL 66 SERVICE STATION

DRAWN BY: H.S.
CHECKED:
APPROVED:
DATE: CWE
PROJECT: 1309
DNR NO: 03-10-
FIGURE
CAD FILE:
